

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010											
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A									
Los Angeles City College																																																					
Total		2,787	05AUG00A	06JUL11	288,401,251																																																
101 Science and Technology Building																																																					
+ Pre-Design/Programming																																																					
		102	01APR02A	21AUG02A	0																																																
+ Project Design																																																					
		946	21OCT02A	03JUL06A	0																																																
+ Project DSA Review																																																					
		798	02SEP03A	18OCT06A	0																																																
+ Project Bid and Award																																																					
		97	04OCT06A	21FEB07	0																																																
+ Project Construction																																																					
		474	08MAR07	19JAN09	52,300,000																																																
+ Project Close-Out																																																					
		1,323	30SEP05A	16DEC10	0																																																
+ Commissioning																																																					
		2,259*	21OCT02A	26DEC08	0																																																
+ FF&E																																																					
		22	16DEC08	16JAN09	0																																																
+																																																					
		2,528*	01APR02A	02MAR09	0																																																
102 Family Life Science																																																					
+ Pre-Design/Programming																																																					
		977	16SEP02A	12JUL06A	0																																																
+ Project Design																																																					
		1,168	02DEC02A	29JUN07	0																																																
+ Project DSA Review																																																					
		192	17JUL07	16APR08	0																																																
+ Project Bid and Award																																																					
		1,315	30SEP05A	06DEC10	0																																																
+ Project Construction																																																					
		260	18FEB09	25FEB10	5,280,000																																																
+ Project Close-Out																																																					
		1,310	30SEP05A	29NOV10	0																																																
+ FF&E																																																					
		12	10FEB10	25FEB10	0																																																

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

Early Bar
 Progress Bar
 Critical Activity

017U
 LACCD
 Los Angeles City College
 Campus Summary

Sheet 1 of 18

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

+																																			
106 Caesar Chavez - Admin Building																																			

+ Pre-Design/Programming																																			
+ Project Design																																			
+ Project DSA Review																																			
+ Project Bid and Award																																			
+ Project Construction																																			
+ Project Close-Out																																			
+ FF&E																																			
+																																			

107 Clausen Hall																																			
------------------	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

107.01 Clausen Hall - DSPS																																			
+ Project Bid and Award																																			
+ Project Construction																																			
+ Project Close-Out																																			
+																																			

107.02 Clausen Hall Modernization																																			
-----------------------------------	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

+ Pre-Design/Programming																																			
+ Project Design																																			
+ Project DSA Review																																			
+ Project Bid and Award																																			

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19




017U
 LACCD
 Los Angeles City College
 Campus Summary

017U
 LACCD
 Los Angeles City College
 Campus Summary

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Close-Out						[Gantt bar from 30SEP05A to 06DEC10]																																						
+ FF&E						[Gantt bar from 05MAR10 to 24MAR10]																																						
+						[Gantt bar from 30JUN06A to 14SEP06A]																																						
110 Holmes Hall						[Summary bar]																																						
+ Project Design						[Gantt bar from 01JUL02A to 06DEC10]																																						
+ Project DSA Review						[Gantt bar from 26DEC03A to 26SEP07]																																						
+ Project Bid and Award						[Gantt bar from 27SEP07 to 26DEC07]																																						
+ Project Construction						[Gantt bar from 10JAN08 to 24OCT08]																																						
+ Project Close-Out						[Gantt bar from 27OCT08 to 07JAN09]																																						
+ FF&E						[Gantt bar from 06OCT08 to 24OCT08]																																						
+						[Gantt bar from 01JUL02A to 07JAN09]																																						
111 Jefferson Hall						[Summary bar]																																						
+ Pre-Design/Programming						[Gantt bar from 25SEP02A to 20DEC02A]																																						
+ Project Design						[Gantt bar from 02APR03A to 23APR07]																																						
+ Project DSA Review						[Gantt bar from 08MAY07 to 19DEC07]																																						
+ Project Bid and Award						[Gantt bar from 30SEP05A to 06DEC10]																																						
+ Project Construction						[Gantt bar from 18FEB09 to 23APR10]																																						
+ Project Close-Out						[Gantt bar from 30SEP05A to 06DEC10]																																						
+ FF&E						[Gantt bar from 29MAR10 to 15APR10]																																						

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

 Early Bar
 Progress Bar
 Critical Activity

017U




LACCD
 Los Angeles City College
 Campus Summary

Sheet 4 of 18

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+																																												
		2,002	25SEP02A	04AUG10	0	[Green bar from Sep 2002 to Aug 2010]																																						
112 Campus-Wide Comp Network for Internet Access																																												
+ Project Design																																												
		77	07JUL03A	21OCT03A	0																																							
+ Project Construction																																												
		368	15DEC03A	24MAY05A	343,246																																							
+ Project Close-Out																																												
		427	25MAY05A	31JAN07	0	[Green bar from May 2005 to Jan 2007]																																						
113 Martin L. King Annex/ Learning Skills Center																																												
+ Pre-Design/Programming																																												
		535	09MAY02A	04JUN04A	0																																							
+ Project Design																																												
		337	30JUN06A	26OCT07	0	[Green bar from Jun 2006 to Oct 2007]																																						
+ Project DSA Review																																												
		212	29OCT07	27AUG08	0	[Green bar from Oct 2007 to Aug 2008]																																						
+ Project Bid and Award																																												
		92	26NOV08	08APR09	0	[Green bar from Nov 2008 to Apr 2009]																																						
+ Project Construction																																												
		270	21DEC09	13JAN11	2,866,277	[Green bar from Dec 2009 to Jan 2011]																																						
+ Project Close-Out																																												
		59	14JAN11	06APR11	0	[Green bar from Jan 2011 to Apr 2011]																																						
+ Commissioning																																												
		1,597*	31AUG06A	13JAN11	0	[Green bar from Aug 2006 to Jan 2011]																																						
+ FF&E																																												
		24	09DEC10	13JAN11	0	[Green bar from Dec 2010 to Jan 2011]																																						
+																																												
		3,215*	09MAY02A	25FEB11	0	[Green bar from May 2002 to Feb 2011]																																						
115 Health, Fitness, PE Building																																												
+ Pre-Design/Programming																																												
		65	01APR02A	30JUN02A	0																																							
+ Project Design																																												
		1,331	01JUL02A	17SEP07	0	[Green bar from Jul 2002 to Sep 2007]																																						
+ Project DSA Review																																												
		1,204	02OCT03A	25JUN08	0	[Green bar from Oct 2003 to Jun 2008]																																						

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19




 Early Bar
 Progress Bar
 Critical Activity

017U
 LACCD
 Los Angeles City College
 Campus Summary

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Bid and Award																																												
		68	26JUN08	01OCT08	0																																							
+ Project Construction																																												
		242	02OCT08	15SEP09	32,002,255																																							
+ Project Close-Out																																												
		1,372	30SEP05A	25FEB11	0																																							
+ Commissioning																																												
		2,532*	11OCT02A	15SEP09	0																																							
+ FF&E																																												
		31	03AUG09	15SEP09	0																																							
+																																												
		1,954	01APR02A	25NOV09	0																																							
116/120/103: Parkg St./PE Bldg/Athletic Fld																																												
+ Pre-Design/Programming																																												
		65	01APR02A	30JUN02A	0																																							
+ Project Design																																												
		234	01JUL02A	27MAY03A	0																																							
+ Project DSA Review																																												
		310	28MAY03A	10AUG04A	0																																							
+ Project Bid and Award																																												
		183	20DEC04A	07SEP05A	0																																							
+ Project Construction																																												
		736	24OCT05A	29OCT07	52,370,000																																							
+ Project Close-Out																																												
		43	30OCT07	02JAN08	0																																							
+ FF&E																																												
		21	01OCT07	29OCT07	0																																							
+																																												
		2,103*	01APR02A	02JAN08	0																																							
117 Student Admissions Center-Terminated																																												
+ Pre-Design/Programming																																												
		59	01APR02A	20JUN02A	0																																							
+ Project Design																																												
		306	18APR02A	24JUN03A	963,263																																							
+ Project DSA Review																																												
		387	07FEB03A	09AUG04A	0																																							

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

 Early Bar
 Progress Bar
 Critical Activity

017U
 LACCD
 Los Angeles City College
 Campus Summary

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010									
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A							
+ Project Bid and Award																								24	27AUG04A	30SEP04A	0																								
+ Project Close-Out																								41	15NOV05A	14JUL06A	0																								
118 Demolition of Chemistry and Pool Building																																																			
+ Project Design																								380	07NOV03A	04MAY05A	133,697																								
119 Parking Structr-Studnt Admissions-Terminated																																																			
+ Pre-Design/Programming																								59	01APR02A	20JUN02A	0																								
+ Project Design																								158	18APR02A	26NOV02A	0																								
+ Project DSA Review																								437	27NOV02A	09AUG04A	936,121																								
+ Project Bid and Award																								511	27AUG04A	31AUG06A	0																								
121 Demolition of Men's Gym Building																																																			
+ Project Design																								90	31JAN07	06JUN07	0																								
+ Project Bid and Award																								286	29AUG08	14OCT09	0																								
+ Project Construction																								881	30JUN06A	18DEC09	0																								
+ Project Close-Out																								66	21DEC09	24MAR10	0																								
+																								1,100*	31JAN07	03FEB10	0																								
122 Child Development Center																																																			
+ Pre-Design/Programming																								15	01SEP03A	19SEP03A	0																								
+ Project Design																								553	22SEP03A	18NOV05A	0																								
+ Project DSA Review																								634	29JAN04A	26JUL06A	0																								

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

Early Bar
 Progress Bar
 Critical Activity

017U

LACCD
 Los Angeles City College
 Campus Summary

Sheet 7 of 18

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Bid and Award																																												
		73	17JUL06A	26OCT06A	0																																							
+ Project Construction																																												
		370	11DEC06A	15DEC07	14,880,000																																							
+ Project Close-Out																																												
		71	17DEC07	26MAR08	0																																							
+																																												
		1,601*	01SEP03A	18JAN08	0																																							
Library Building - State Funded																																												
+ Pre-Design/Programming																																												
		495	30APR02A	30MAR04A	0																																							
+ Project Design																																												
		159	01APR04A	12NOV04A	0																																							
+ Project DSA Review																																												
		270	17NOV04A	12DEC05A	0																																							
+ Project Bid and Award																																												
		102	03JAN06A	24MAY06A	0																																							
+ Project Construction																																												
		540	05JUL06A	26DEC07	3,768,778																																							
+ Project Close-Out																																												
		69	27DEC07	02APR08	0																																							
+																																												
		2,124*	30APR02A	21FEB08	0																																							
130 Women's Gym Renovation																																												
+ Pre-Design/Programming																																												
		802	01MAR04A	25APR07	0																																							
+ Project Design																																												
		248	26APR07	16APR08	0																																							
+ Project DSA Review																																												
		155	24APR08	03DEC08	0																																							
+ Project Bid and Award																																												
		191	10DEC08	09SEP09	0																																							
+ Project Construction																																												
		235	16SEP09	18AUG10	34,000																																							
+ Project Close-Out																																												
		82	19AUG10	15DEC10	0																																							

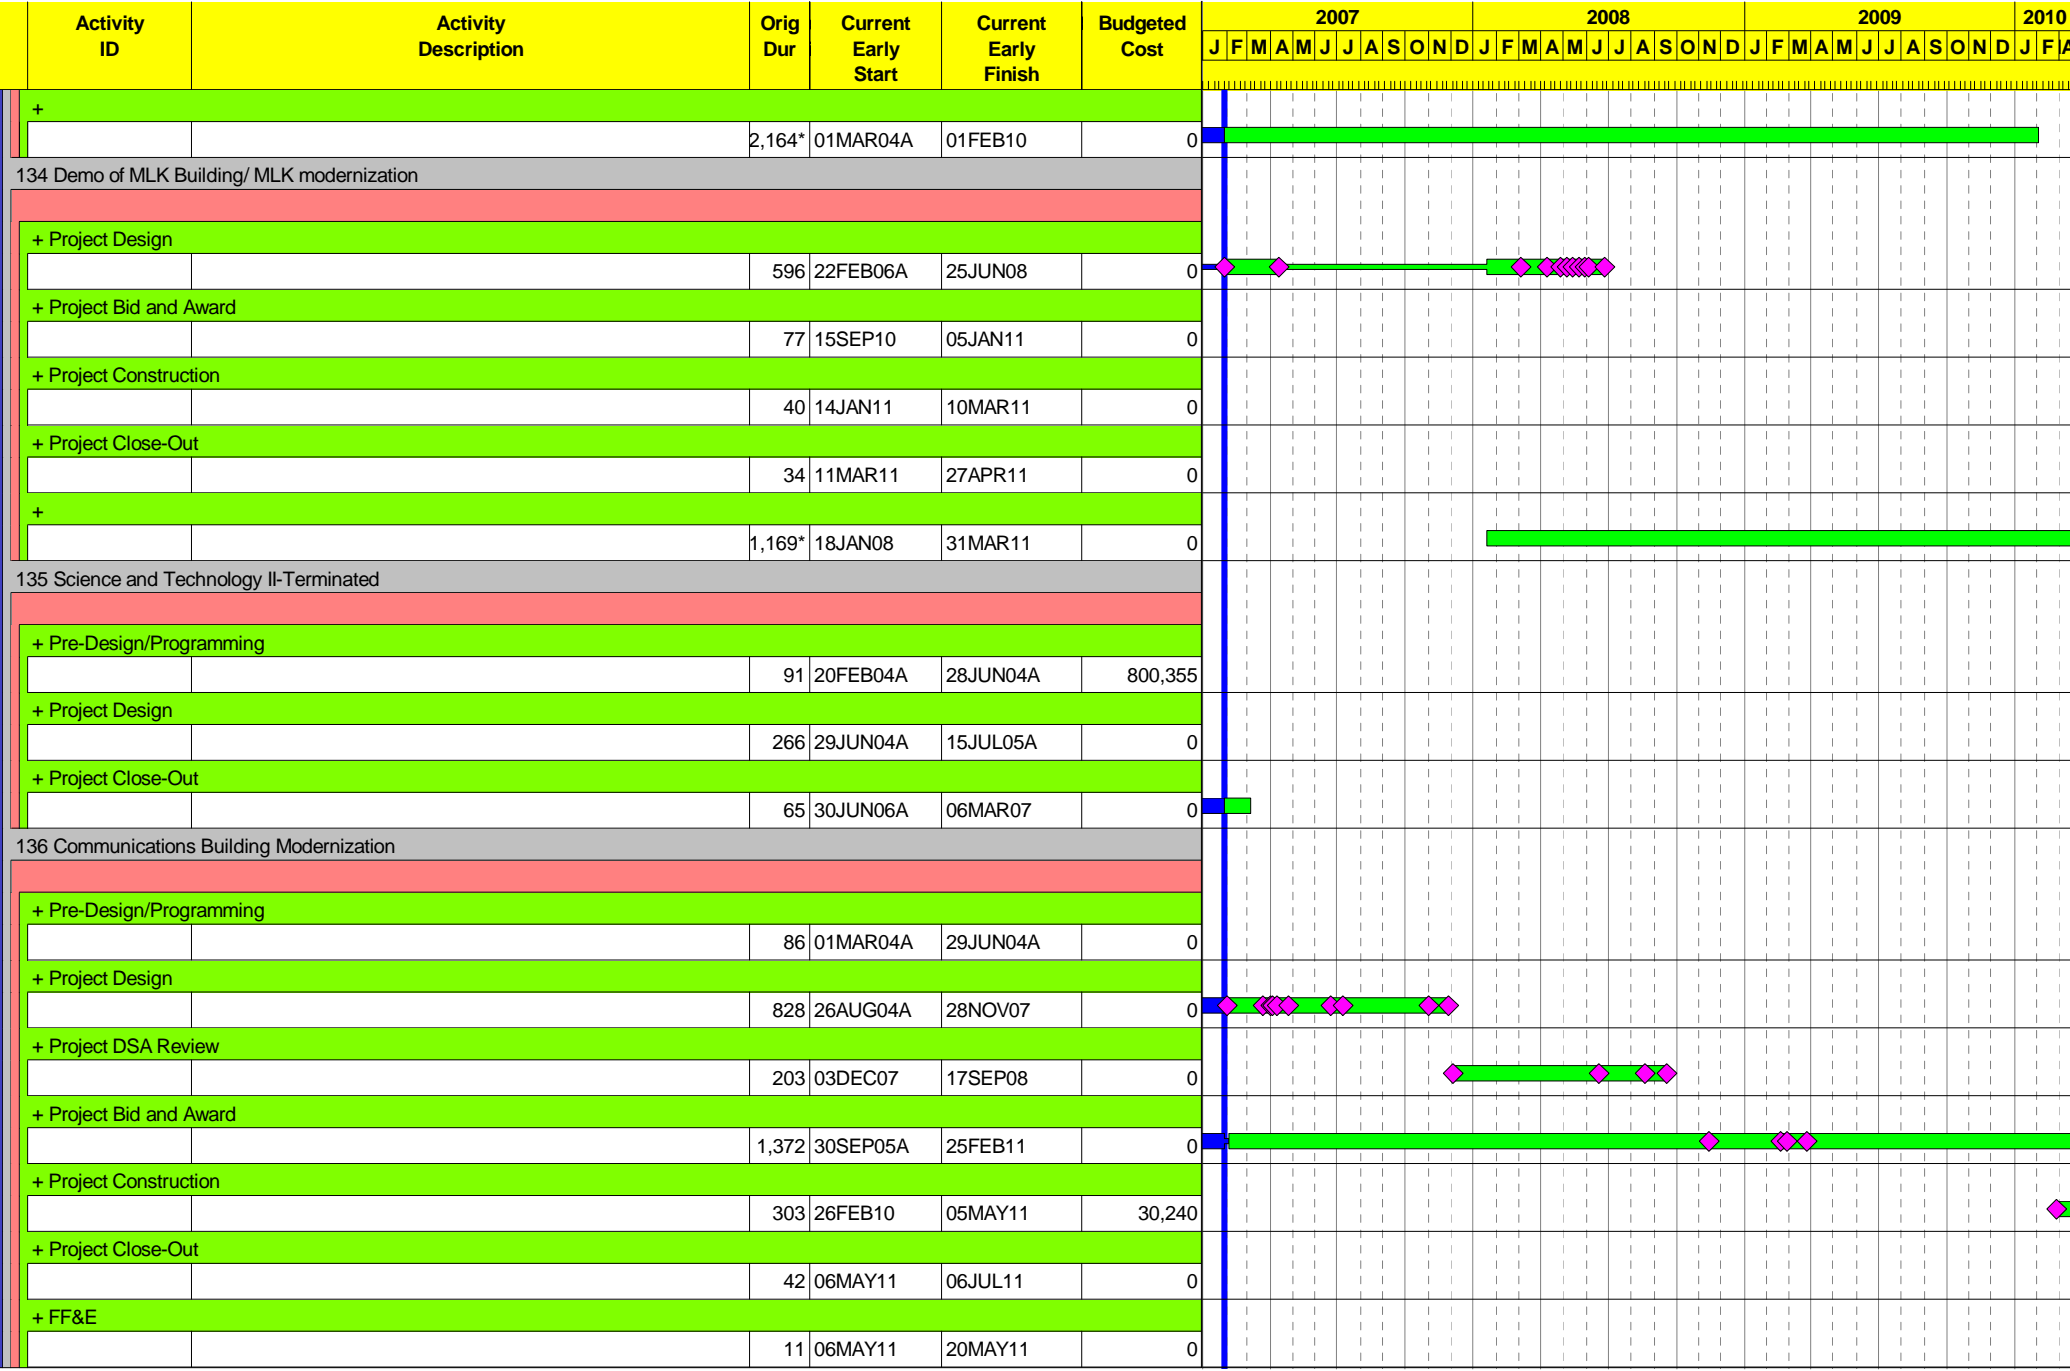
Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

Early Bar
 Progress Bar
 Critical Activity




017U
 LACCD
 Los Angeles City College
 Campus Summary

Sheet 8 of 18

Date	Revision	Checked	Approved



Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

 Early Bar
 Progress Bar
 Critical Activity




017U
 LACCD
 Los Angeles City College
 Campus Summary

Sheet 10 of 18

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+																																												
		2,651*	01MAR04A	03JUN11	0	[Green Bar]																																						
170 Master Planning																																												
+ Master Plan																																												
		217	01AUG01A	31MAY02A	606,016																																							
172 Emergency Lighting, Fire Alarm & Sec Systems																																												
+ Project Construction																																												
		1,871	22OCT03A	03MAR11	173,239	[Green Bar]																																						
+ Project Close-Out																																												
		1,786	26FEB04A	09MAR11	0	[Blue Bar]																																						
173 RWGPL																																												
173.01 RWGPL - Site Utilities Infrastructure																																												
+ Project Design																																												
		236	16AUG04A	20JUL05A	0																																							
+ Project Construction																																												
		1,413	16AUG04A	10MAR10	13,340,550	[Green Bar]																																						
+ Project Close-Out																																												
		40	11MAR10	05MAY10	0	[Green Bar]																																						
173.02 RWGPL - Landscaping Cntrl Wk and N. Quad																																												
+ Project Design																																												
		834	15JUN04A	26SEP07	0	[Green Bar]																																						
+ Project Bid and Award																																												
		84	02NOV09	03MAR10	0	[Green Bar]																																						
+ Project Construction																																												
		70	28DEC10	05APR11	90,000	[Green Bar]																																						
+ Project Close-Out																																												
		45	06APR11	08JUN11	0	[Green Bar]																																						
+																																												
		2,515*	15JUN04A	04MAY11	0	[Green Bar]																																						
173.03 RWGPL - Landscaping North Entry Plaza																																												
+ Project Design																																												
		873	15JUN04A	20NOV07	0	[Green Bar]																																						
+ Project DSA Review																																												
		160	21NOV07	09JUL08	0	[Green Bar]																																						
+ Project Bid and Award																																												
		94	17JUL08	26NOV08	0	[Green Bar]																																						

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

 Early Bar
 Progress Bar
 Critical Activity

017U
 LACCD
 Los Angeles City College
 Campus Summary

Sheet 11 of 18

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Construction																																												
+ Project Close-Out																																												
+																																												
173.04 RWGPL- Landscaping N. Gte & Wil. Brk Edge																																												
+ Project Design																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
+																																												
173.05 RWGPL - Landscaping North of East Walk																																												
+ Project Design																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
+																																												
173.06 RWGPL - Landscaping around Cafeteria																																												
+ Project Design																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
+																																												

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19




Early Bar
 Progress Bar
 Critical Activity

017U
 LACCD
 Los Angeles City College
 Campus Summary

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
173.08 Replace Electrical at Chem Demolition																																												
+ Project Design																																												
		166	20SEP04A	13MAY05A	43,207																																							
174 Signage for Safety and Public Information																																												
+ Project Design																																												
		854	15JUN04A	24OCT07	0																																							
+ Project Bid and Award																																												
		54	16DEC09	03MAR10	0																																							
+ Project Construction																																												
		70	28DEC10	05APR11	80,818																																							
+ Project Close-Out																																												
		45	06APR11	08JUN11	0																																							
+																																												
		2,515*	15JUN04A	04MAY11	0																																							
175 Restrooms Modernization																																												
+ Project Design																																												
		284	01JUL02A	06AUG03A	0																																							
+ Project DSA Review																																												
		129	28MAY03A	25NOV03A	0																																							
+ Project Bid and Award																																												
		57	05DEC03A	25FEB04A	0																																							
+ Project Construction																																												
		681	15MAR04A	15NOV06A	1,190,039																																							
+ Project Close-Out																																												
		13	30OCT06A	15NOV06A	0																																							
+																																												
		1,599*	01JUL02A	15NOV06A	0																																							
176 Demolition of Temp / Obsolete Facilities																																												
176.01 Demolition of Maintenance Bungalows																																												
+ Project Design																																												
		53	16OCT02A	30DEC02A	0																																							
+ Project Construction																																												
		6	23DEC02A	31DEC02A	118,475																																							
176.02 Demolition of Tennis Courts, Bungalows																																												
+ Project Construction																																												
		44	14APR03A	12JUN03A	258,628																																							

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

 Early Bar
 Progress Bar
 Critical Activity

017U

LACCD
 Los Angeles City College
 Campus Summary

Sheet 13 of 18

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
179.05 Campus Imprvmnts - Elec.Infrastructure																																												
+ Project Construction																																												
		1,157	30JUN06A	21JAN11	0																																							
+ Project Close-Out																																												
		33	24JAN11	09MAR11	0																																							
180 Site Survey and Infrastructure Studies																																												
+ Project Construction																																												
		1,324	03JUN02A	08AUG07	310,382																																							
+ Project Close-Out																																												
		44	09AUG07	10OCT07	0																																							
181 Environmental Impact Report (EIR)																																												
+ EIR / CEQA																																												
		1,295	10JAN02A	02FEB07	287,605																																							
182 CEQA																																												
+ EIR / CEQA																																												
		1	29NOV02A	29NOV02A	47																																							
189 Asset Assessment and Move Management																																												
+ Project Construction																																												
		2,338	01JAN02A	04MAR11	2,018,291																																							
190 Program Management																																												
+ Program / Project Management																																												
		2,338	01JAN02A	04MAR11	2,252,494																																							
191 Project Management																																												
+ Program / Project Management																																												
		2,787	05AUG00A	06JUL11	14,867,545																																							
192 Reimbursables																																												
+ Project Construction																																												
		153	05AUG00A	10MAR01A	0																																							
193 Legal Services																																												
+ Project Construction																																												
		2,338	01JAN02A	04MAR11	3,664,423																																							

Start Date 01AUG00
 Finish Date 06JUL11
 Data Date 31JAN07
 Run Date 02MAR07 12:19

Early Bar
 Progress Bar
 Critical Activity

017U
 LACCD
 Los Angeles City College
 Campus Summary

Sheet 17 of 18

Date	Revision	Checked	Approved

