




Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010											
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A									
East Los Angeles College																																																					
Subtotal		2,344	01JAN02A	14MAR11	324,615,693																																																
201 Health Care Careers Center																																																					
+ Pre-Design/Programming Phase																																																					
		597	08FEB02A	04JUN04A	22,585																																																
202 Parking Structure Lot 3																																																					
+ Pre-Design/Programming Phase																																																					
		336	01JAN02A	22APR03A	11,265																																																
+ Design Phase																																																					
		448	23APR03A	21JAN05A	1,325,025																																																
+ DSA Review Phase																																																					
		584	22JAN05A	09MAY07	219,075																																																
+ Bid/Award Phase																																																					
		62	10MAY07	08AUG07	13,900																																																
+ Construction Phase																																																					
		319	09AUG07	07NOV08	32,912,000																																																
+ Closeout Phase																																																					
		74	10NOV08	24FEB09	0																																																
203 Physical Plant Building																																																					
+ Design Phase																																																					
		580	09OCT03A	18JAN06A	511,315																																																
+ DSA Review Phase																																																					
		348	30SEP05A	13FEB07	21,837																																																
+ Bid/Award Phase																																																					
		82	23OCT06A	16FEB07	3,500																																																
+ Construction Phase																																																					
		105	19FEB07	18JUL07	2,810,882																																																
+ FF&E																																																					
		200	31JAN07	12NOV07	247,002																																																
+ Closeout Phase																																																					
		82	19JUL07	12NOV07	0																																																
205 Parking Structure Lot 4 - Northeast																																																					
+ Pre-Design/Programming Phase																																																					
		351*	01JAN02A	18DEC02A	11,265																																																


Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32

 Early Bar  
 Progress Bar  
 Critical Activity

7E01  
 LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 1 of 21

Date	Revision	Checked	Approved

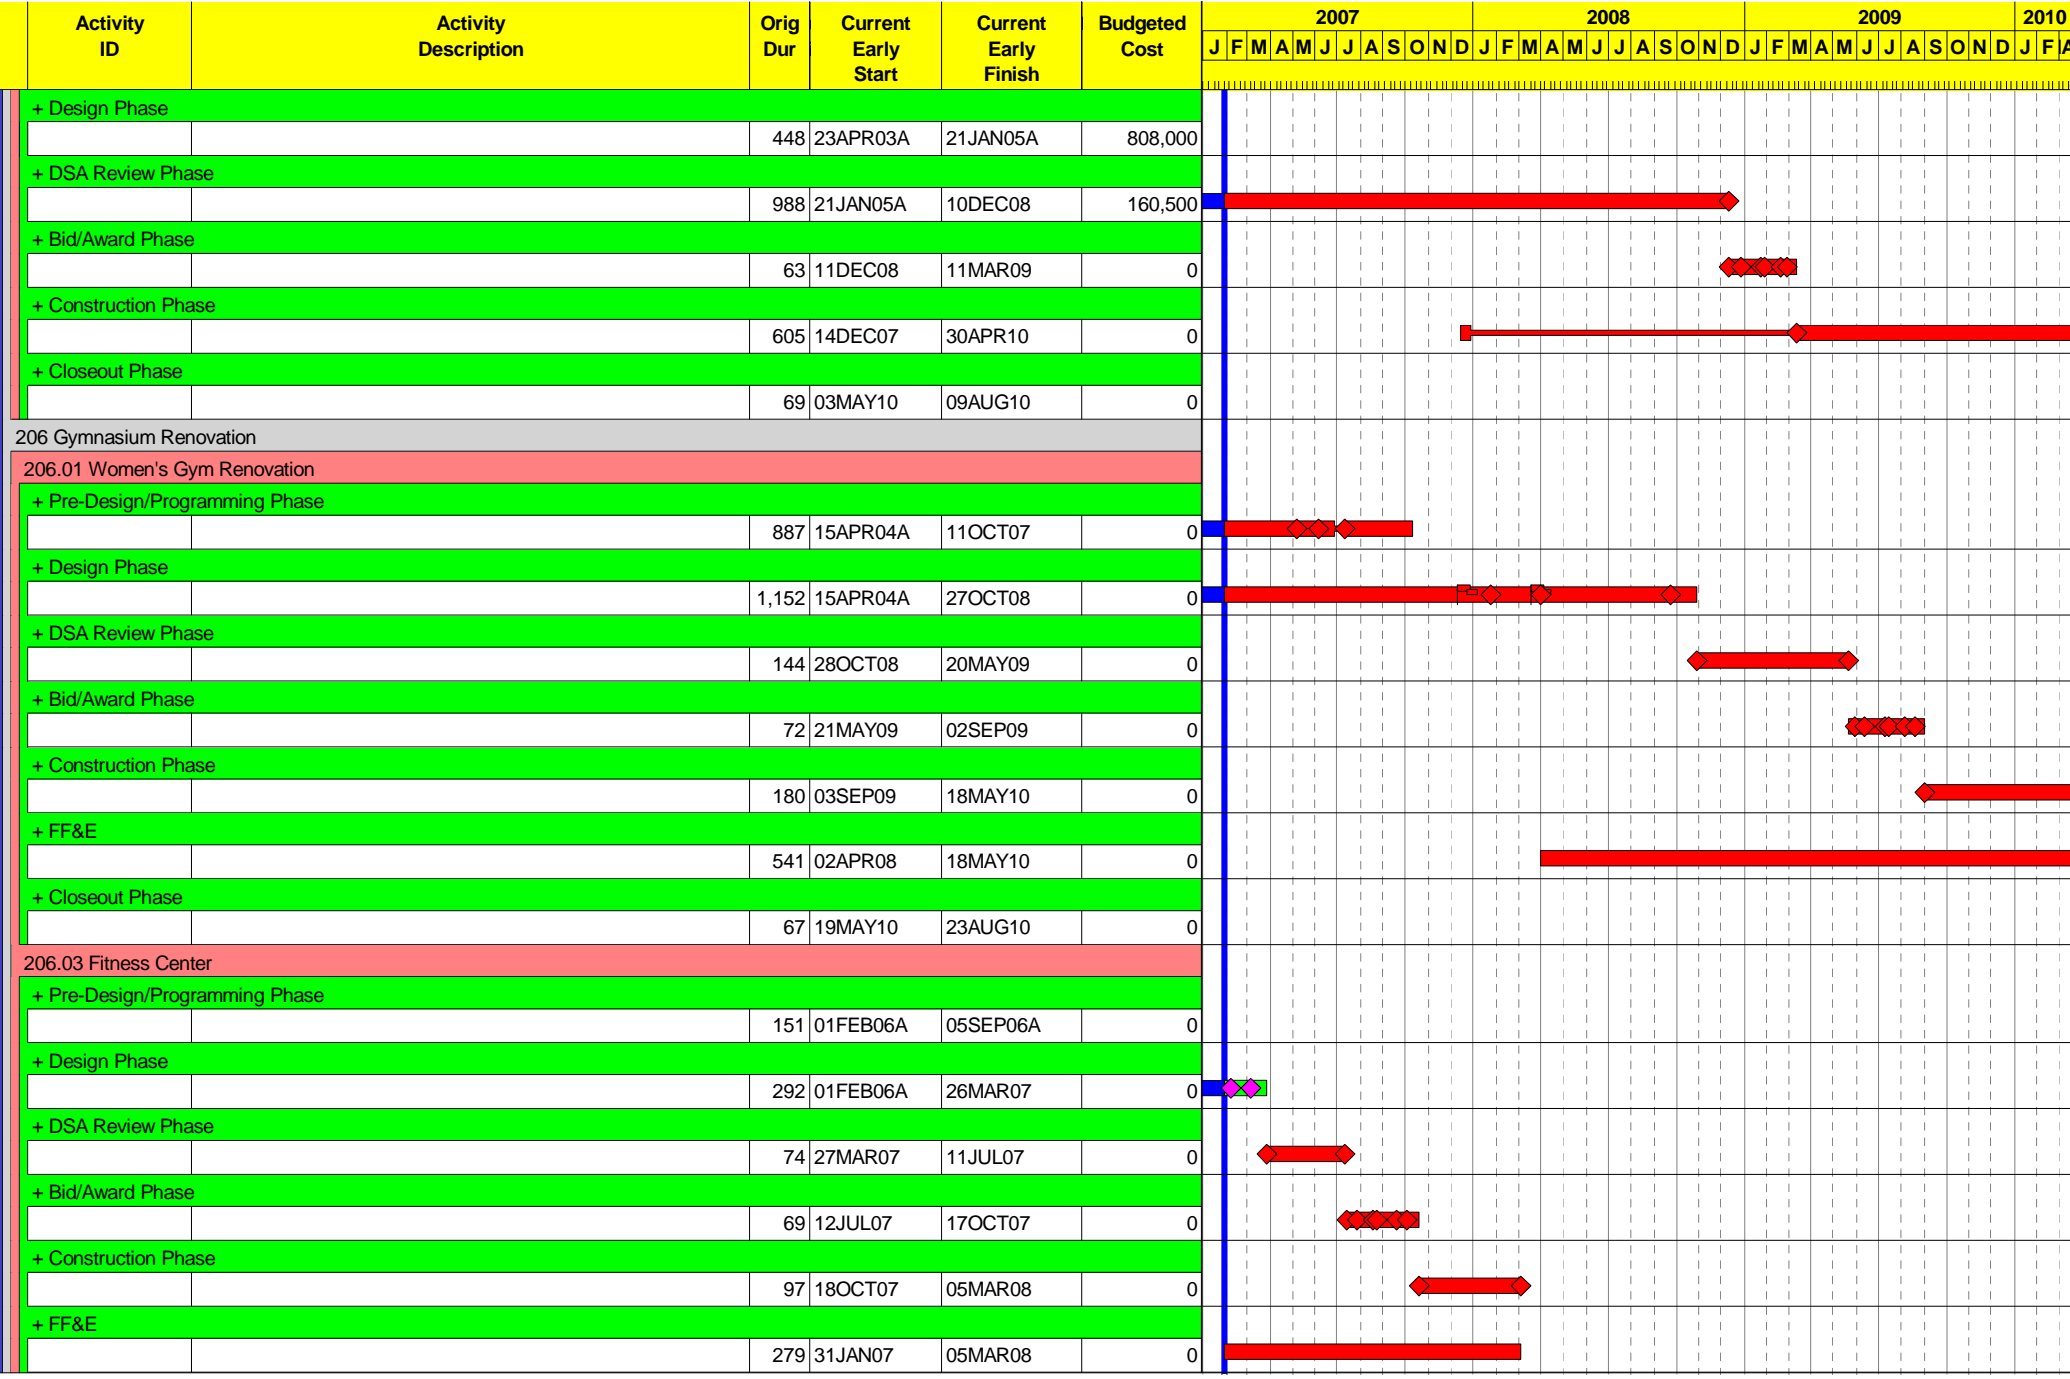


Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32

Early Bar  
 Progress Bar  
 Critical Activity

7E01  
 LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 2 of 21

Date	Revision	Checked	Approved

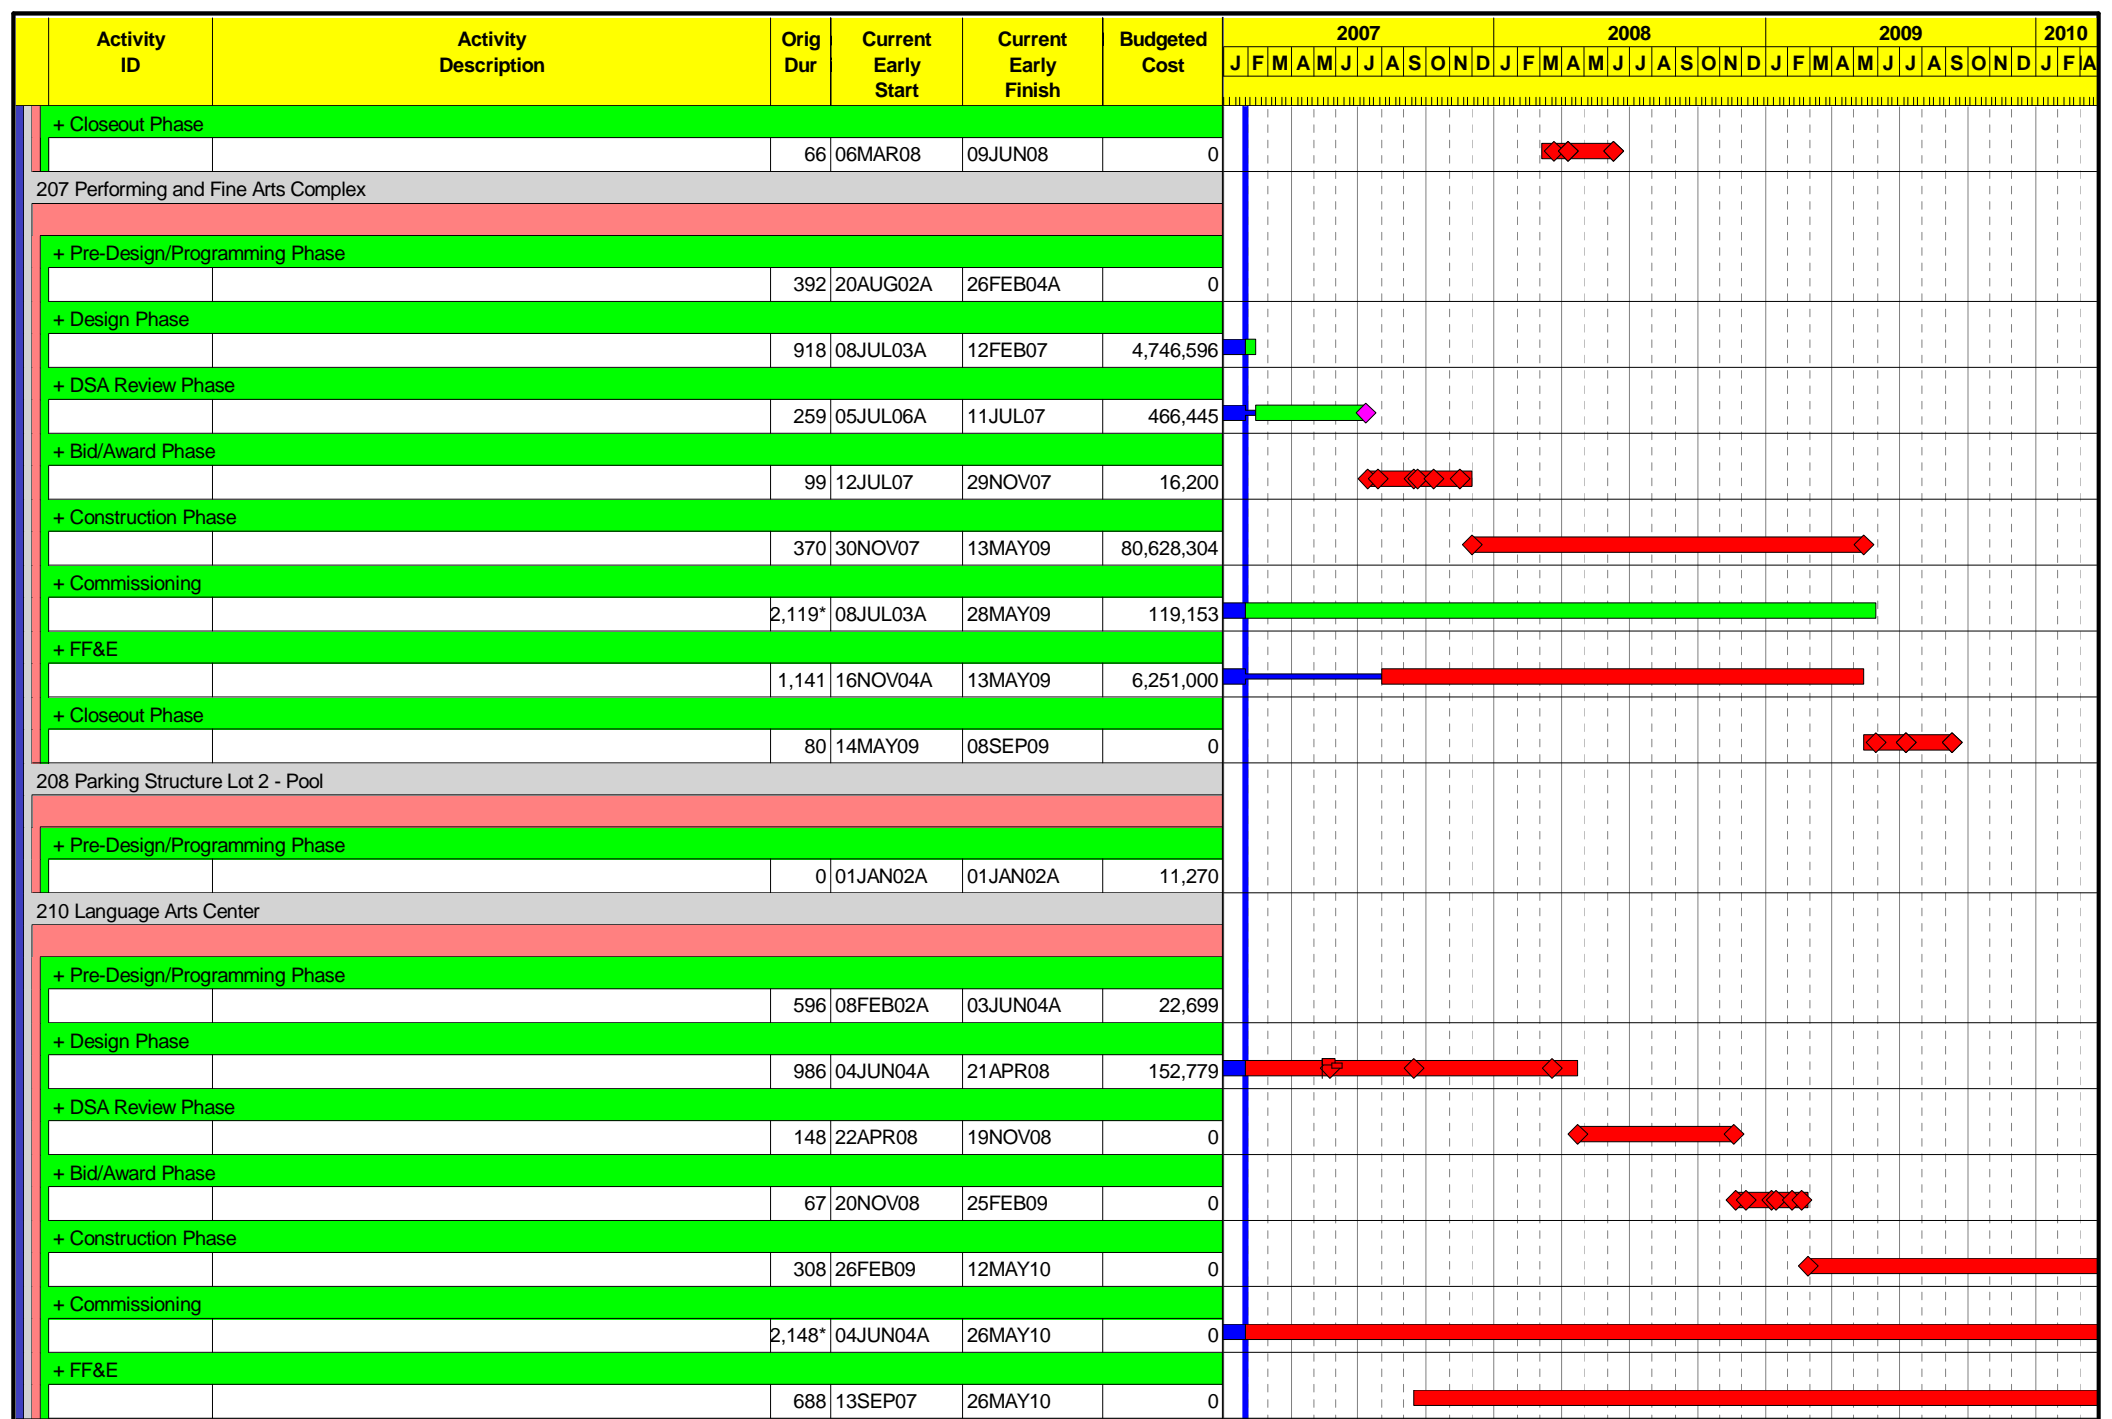

Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32

Early Bar  
 Progress Bar  
 Critical Activity




7E01  
 LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 3 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010									
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A							
+ Closeout Phase																								67	13MAY10	17AUG10	0																								
211 PE Fields Renovation																																																			
211.01 PE Fields-Stadium Synthetic Turf																																																			
+ Bid/Award Phase																								37	31MAY02A	24JUL02A	0																								
+ Construction Phase																								27	25JUL02A	30AUG02A	758,834																								
+ Closeout Phase																								39	30AUG02A	23OCT02A	0																								
211.02 PE Fields-Track and Field Events																																																			
+ Pre-Design/Programming Phase																								47	27JUL02A	01OCT02A	0																								
+ Design Phase																								61	14OCT02A	08JAN03A	29,205																								
+ Bid/Award Phase																								84	23DEC02A	21APR03A	0																								
+ Construction Phase																								140	01MAY03A	15NOV03A	1,014,992																								
+ Closeout Phase																								87	26AUG03A	24DEC03A	0																								
211.03 RETIRED PE Fields-Baseball Safety Fencing																																																			
+ Design Phase																								2,195	01AUG02A	14MAR11	15,375																								
211.04 New Shower Restroom Facility and Baseball																																																			
+ Pre-Design/Programming Phase																								72	18SEP02A	27DEC02A	0																								
+ Design Phase																								327	01NOV02A	10FEB04A	144,600																								
+ DSA Review Phase																								221	02APR03A	10FEB04A	16,149																								
+ Bid/Award Phase																								78	21APR04A	10AUG04A	2,400																								
+ Construction Phase																								476	17JUN04A	01MAY06A	2,126,701																								
+ Commissioning																								57	01DEC05A	21FEB06A	0																								
+ Closeout Phase																								1,157	18SEP02A	31MAR07	0																								

Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32

 Early Bar  
 Progress Bar  
 Critical Activity

7E01  
 LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 4 of 21

Date	Revision	Checked	Approved












Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
216 Community Outreach Educational Center																																												
+ Pre-Design/Programming Phase																																												
		24	01JAN02A	01FEB02A	13,530																																							
217 Student Services Building E1																																												
+ Pre-Design/Programming Phase																																												
		697*	26FEB04A	03FEB06A	1,712,483																																							
+ DSA Review Phase																																												
		443*	15FEB06A	09MAY07	92,482																																							
+ Bid/Award Phase																																												
		96*	10MAY07	15AUG07	6,300																																							
+ Construction Phase																																												
		282	16AUG07	24SEP08	13,947,660																																							
+ Commissioning																																												
		594*	31JAN07	24SEP08	115,126																																							
+ FF&E																																												
		420	31JAN07	24SEP08	1,242,000																																							
+ Closeout Phase																																												
		72	25SEP08	07JAN09	0																																							
218 Academic Network Integrated Backbone																																												
+ Pre-Design/Programming Phase																																												
		229	06FEB03A	26DEC03A	0																																							
+ Design Phase																																												
		565	30DEC03A	17MAR06A	467,600																																							
+ DSA Review Phase																																												
		276	06FEB06A	07MAR07	18,180																																							
+ Bid/Award Phase																																												
		104	31JAN07	27JUN07	3,500																																							
+ Construction Phase																																												
		618	14JUN07	17NOV09	2,230,480																																							
+ Closeout Phase																																												
		492	25JAN08	31DEC09	0																																							
219 Technology Center																																												
219.01 Technology Center																																												
+ Construction Phase																																												
		360	14OCT02A	30AUG04A	10,217,821																																							

Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32


 Early Bar  
 Progress Bar  
 Critical Activity

7E01  
 LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 9 of 21


Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

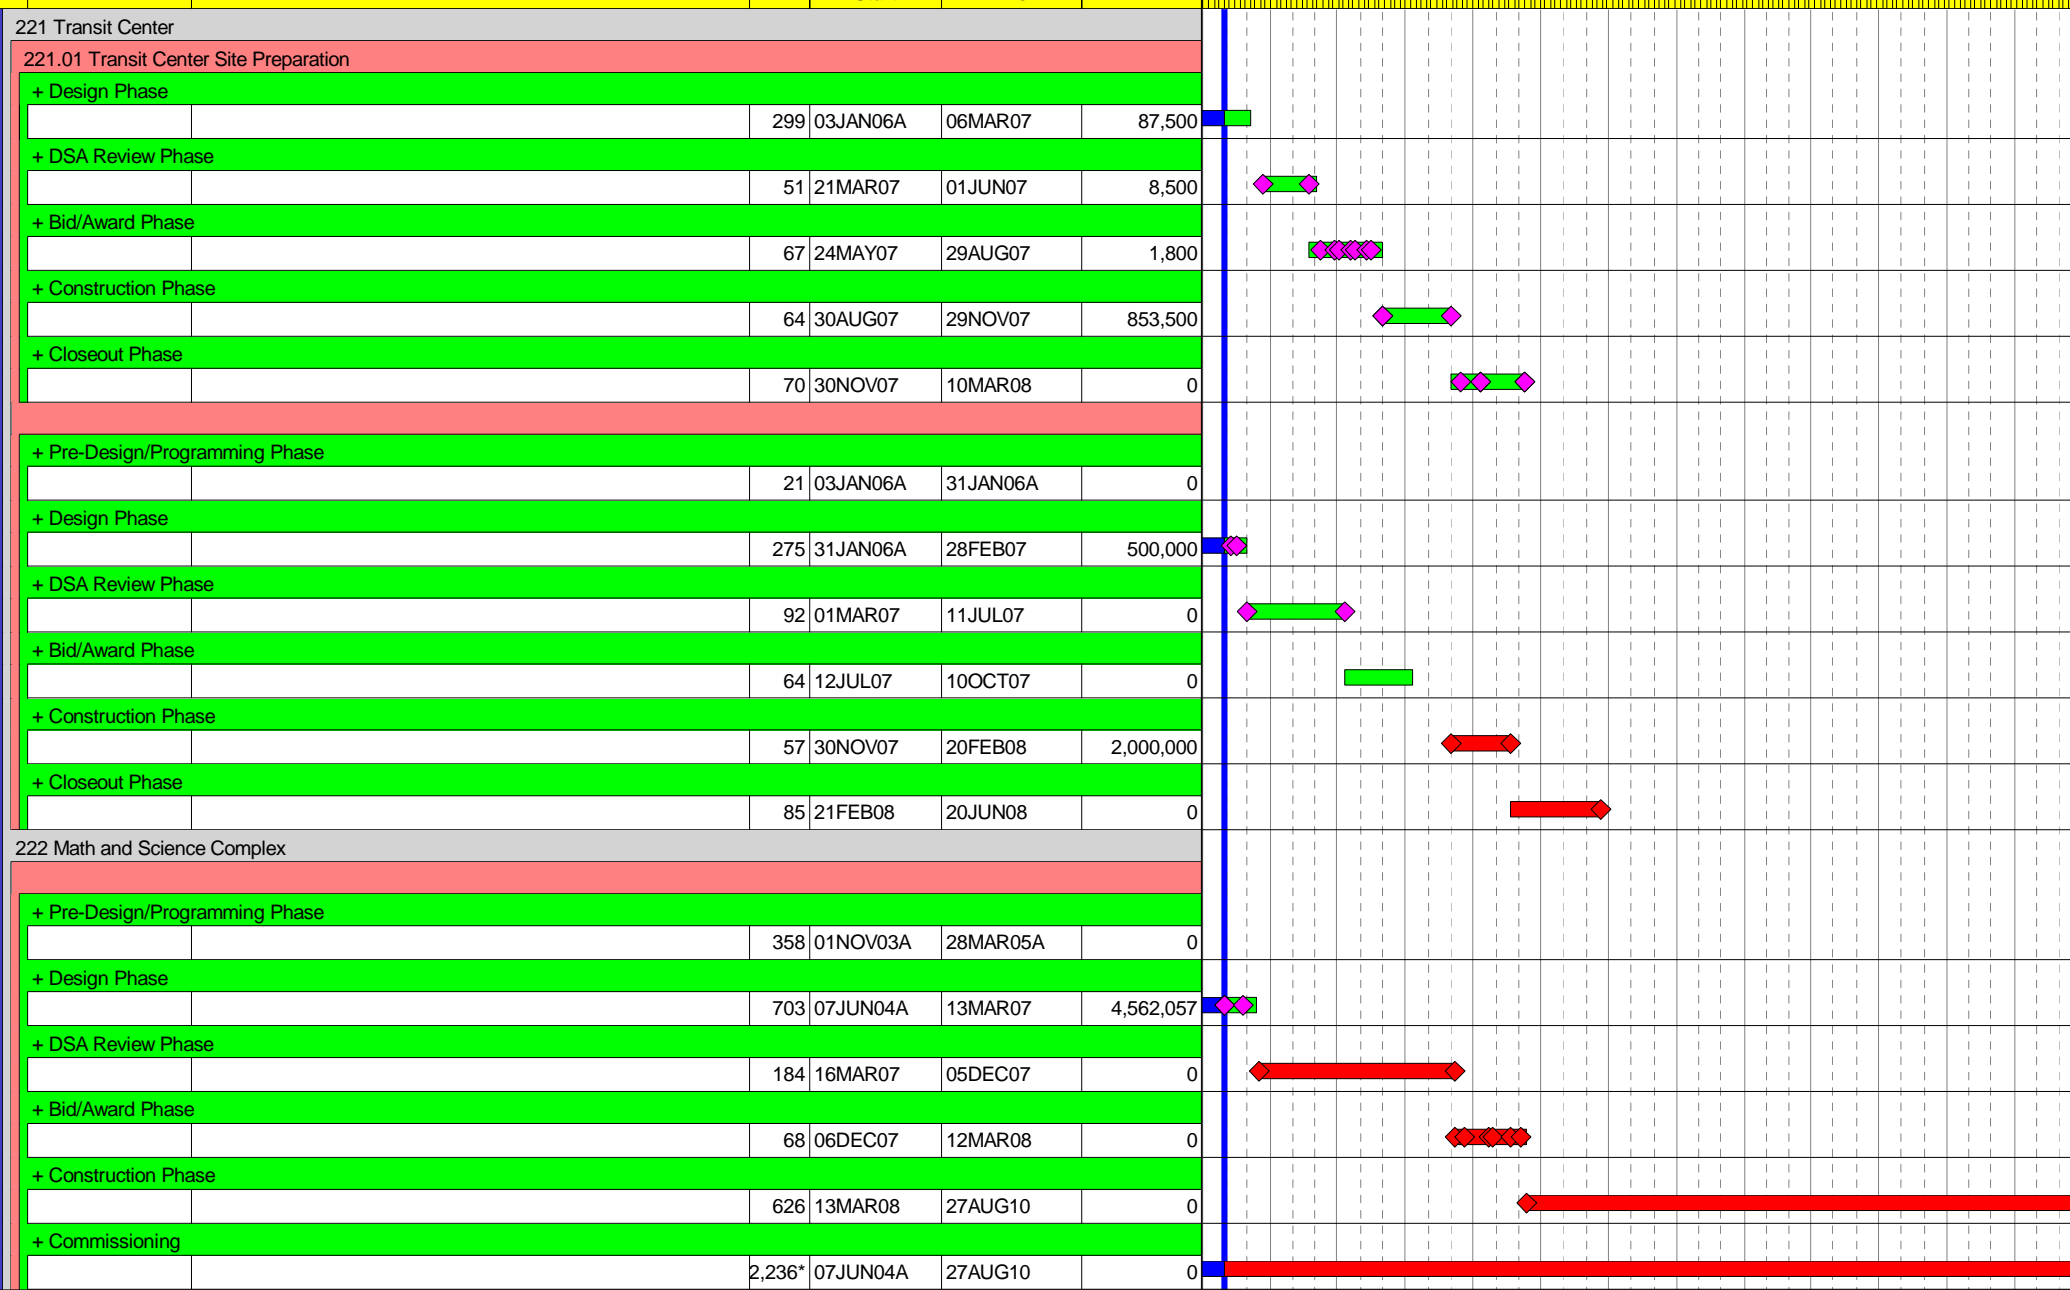

Start Date	01JAN02	Early Bar Progress Bar Critical Activity	7E01	LACCD East Los Angeles College Campus Summary	Sheet 10 of 21	Date	Revision	Checked	Approved
Finish Date	14MAR11								
Data Date	31JAN07								
Run Date	02MAR07 12:32								

© Primavera Systems, Inc.

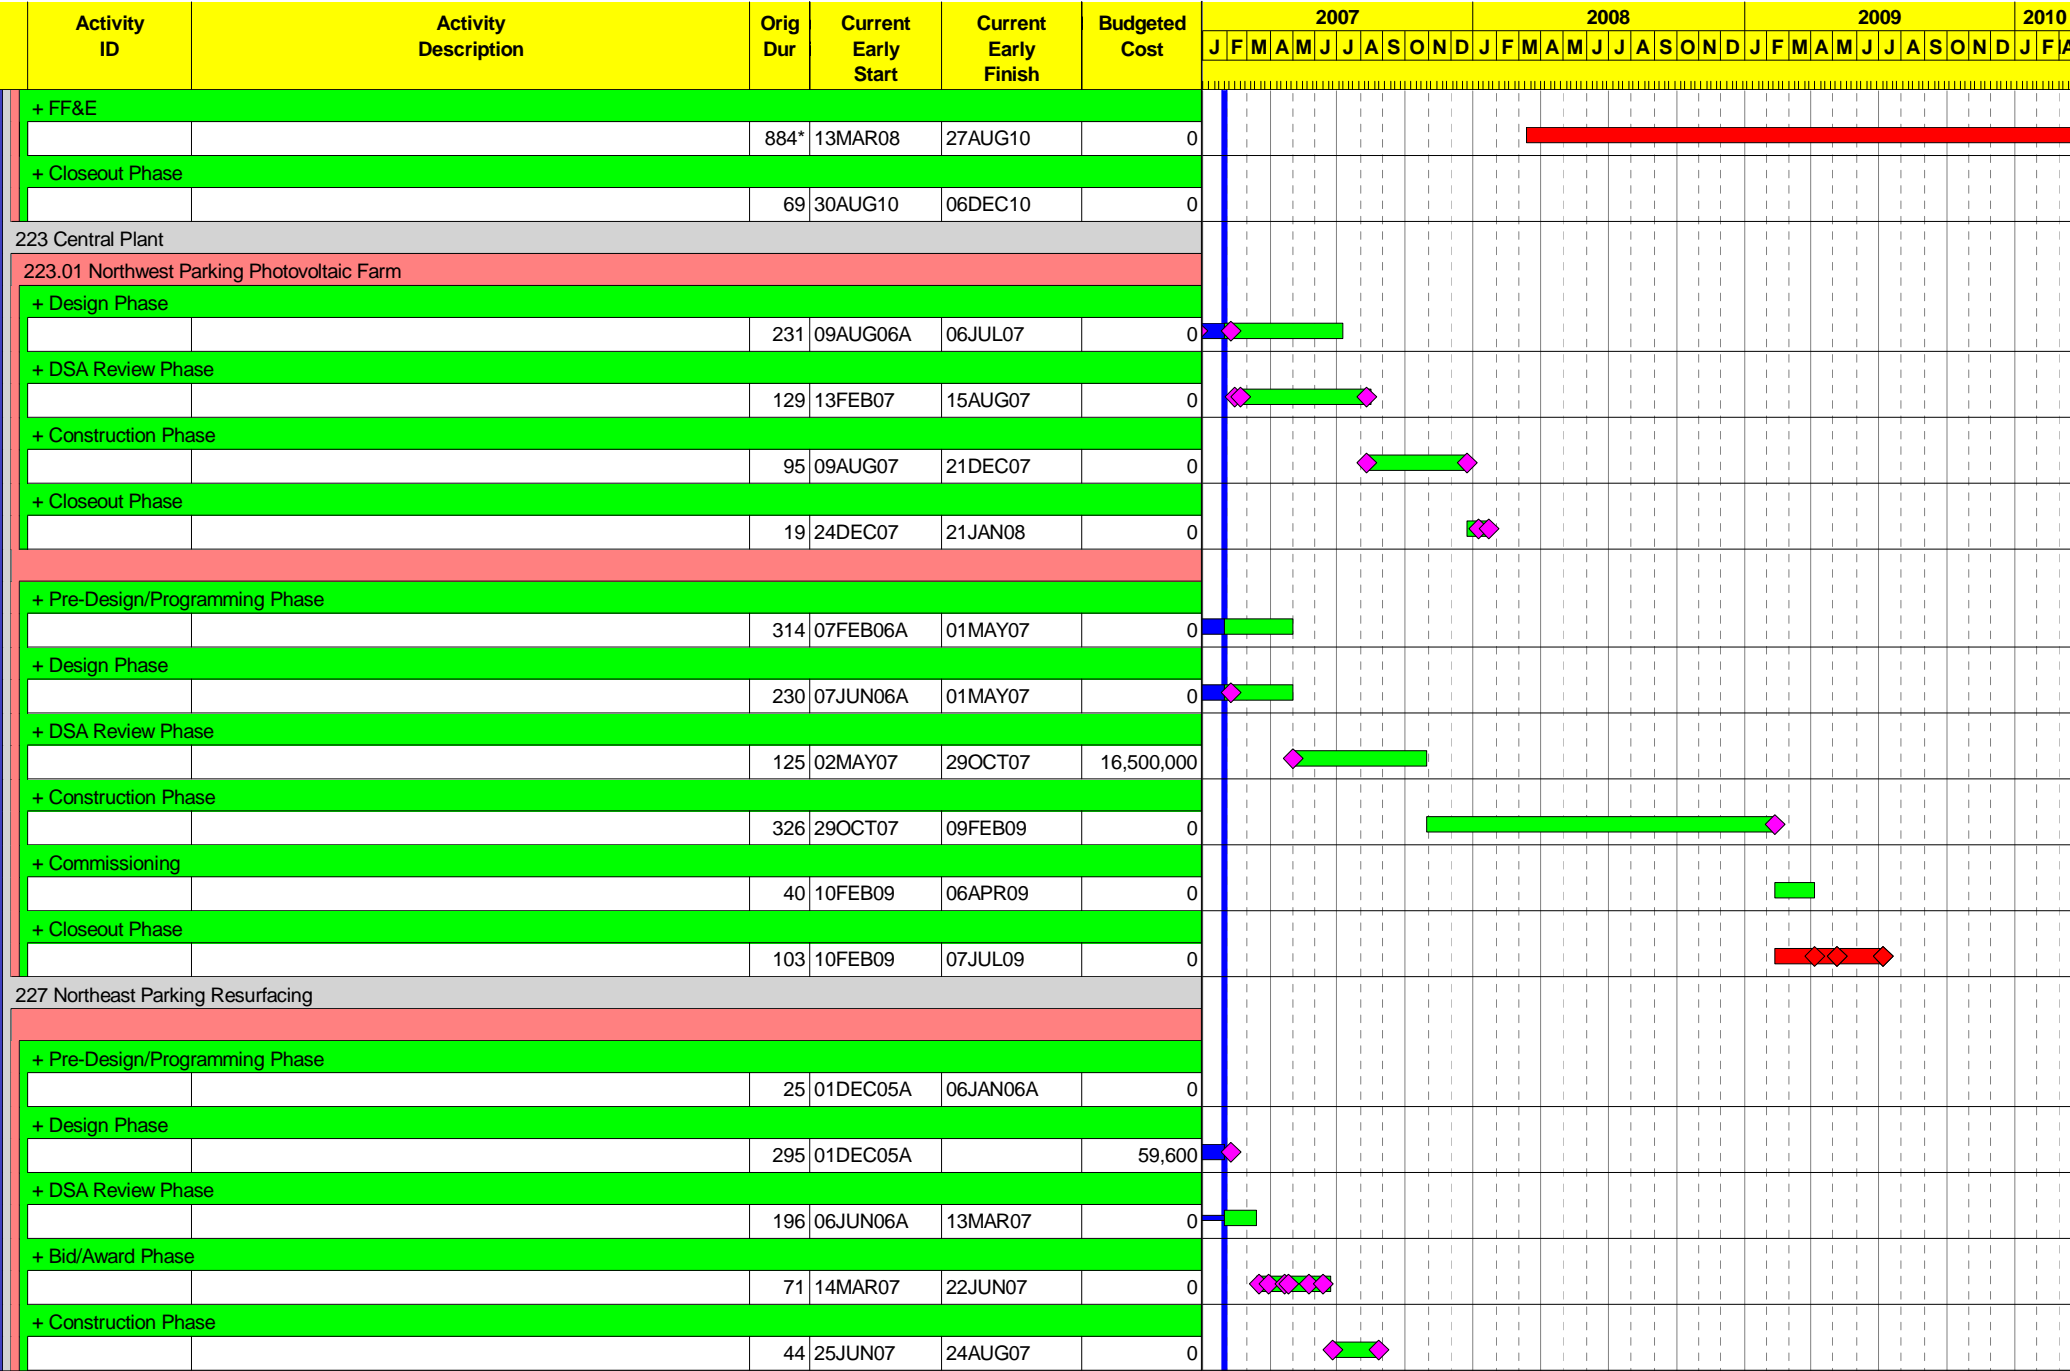

Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32

Early Bar  
 Progress Bar  
 Critical Activity

7E01

LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 11 of 21

Date	Revision	Checked	Approved












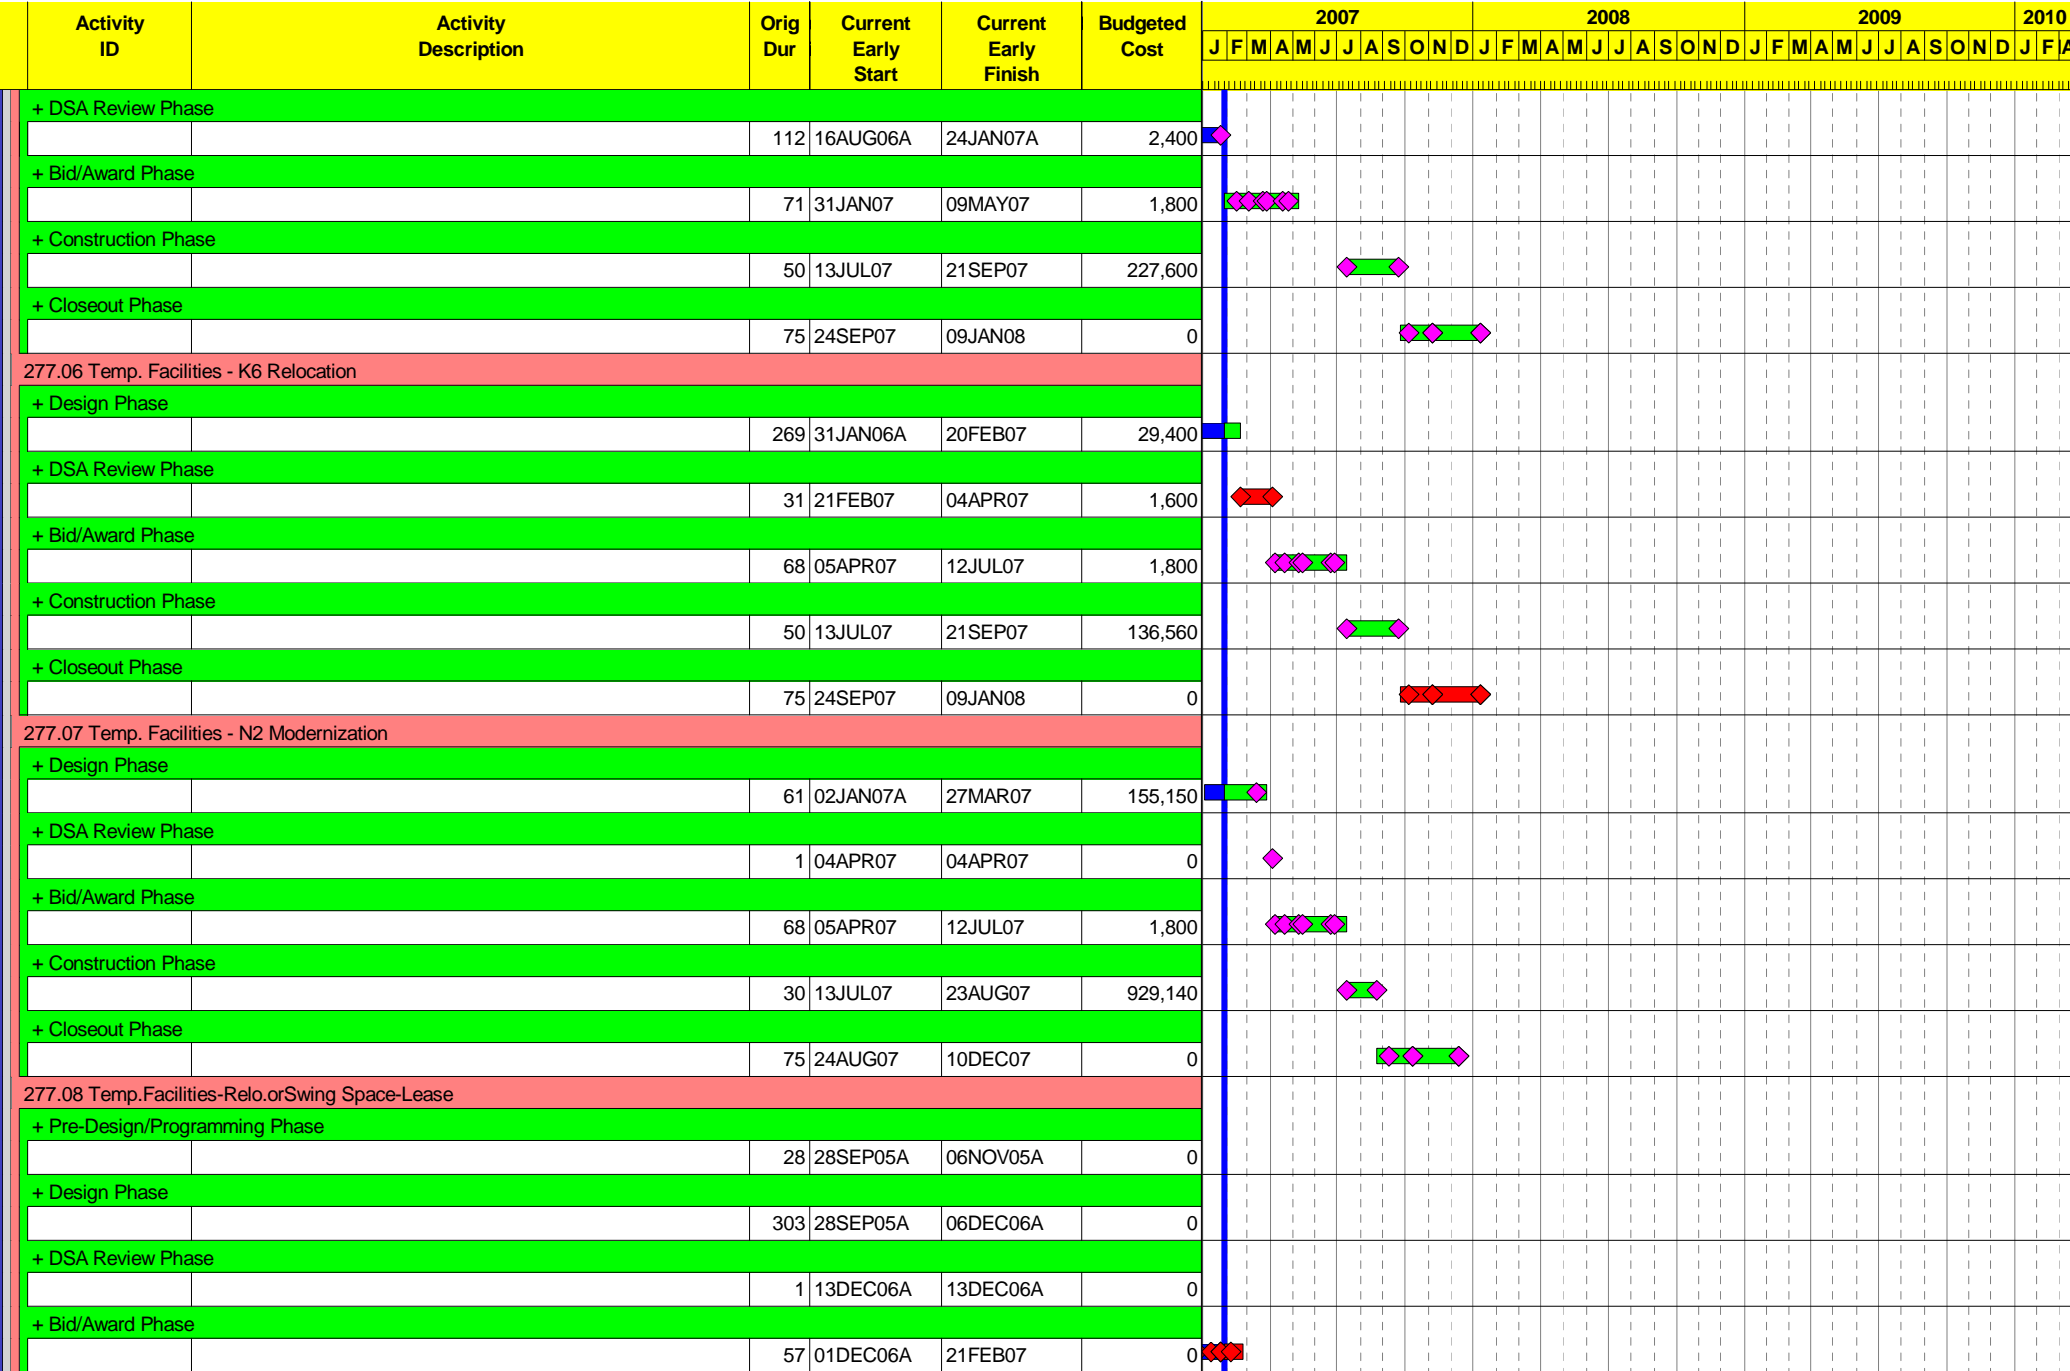

Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32

Early Bar  
 Progress Bar  
 Critical Activity




7E01  
 LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 17 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010									
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A							
+ Construction Phase																								808	22FEB07	27APR10	0	[Red bar]																							
279 Campus Improvements																																																			
279.01 Campus Improvements - General																																																			
+ Construction Phase																								0	01JAN02A		0																								
279.03 C.I. - E3 & E5 Multimedia Conversion																																																			
+ Pre-Design/Programming Phase																								946	22JAN02A	30SEP05A	0																								
+ Design Phase																								132	28FEB03A	03SEP03A	28,034																								
+ DSA Review Phase																								150	29JUL03A	25FEB04A	3,295																								
+ Bid/Award Phase																								135	06APR04A	14OCT04A	0																								
+ Construction Phase																								120	08SEP04A	25FEB05A	560,240																								
+ FF&E																								466	29MAY03A	24MAR05A	0																								
+ Closeout Phase																								161	14FEB05A	30SEP05A	0																								
279.04 C.I.- F,G,H,&K Mech & Elec Upgrades																																																			
+ Pre-Design/Programming Phase																								112	17JUL02A	19DEC02A	0																								
+ Design Phase																								296	19DEC02A	15FEB04A	187,728																								
+ DSA Review Phase																								145	24JUL03A	15FEB04A	6,965																								
+ Bid/Award Phase																								388	03DEC03A	10JUN05A	0																								
+ Construction Phase																								124	27MAY05A	22NOV05A	1,020,242																								
+ Closeout Phase																								344	22NOV05A	31MAR07	0	[Red bar]																							
279.05 C.I. - SCE Transformer Upgrades																																																			
+ Construction Phase																								20	11NOV02A	31DEC02A	322,659																								
279.08 C.I. - Tech Center Central Quad																																																			
+ Pre-Design/Programming Phase																								294	04FEB03A	25MAR04A	0																								

Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32

 Early Bar  
 Progress Bar  
 Critical Activity

7E01  
 LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 18 of 21

Date	Revision	Checked	Approved



Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
279.20 G&H Mechanical & Electrical Upgrades																																												
+ Design Phase																																												
		1,151	01SEP06A	14MAR11	0	[Critical Activity Bar]																																						
+ Bid/Award Phase																																												
		67	14FEB07	17MAY07	0	[Early Bar]																																						
+ Construction Phase																																												
		54	18MAY07	06AUG07	0	[Early Bar]																																						
+ Closeout Phase																																												
		74	24JUL07	05NOV07	0	[Early Bar]																																						
280 Site Survey & Infrastructure Studies																																												
+ Pre-Design/Programming Phase																																												
		76	06FEB03A	22MAY03A	97,179																																							
281 Environmental Impact Report (EIR)																																												
+ Pre-Design/Programming Phase																																												
		316	01JUL03A	22SEP04A	21,950																																							
289 Assesst Assessment & Move Management																																												
+ FF&E																																												
		2,344*	01JAN02A	14MAR11	387,125	[Critical Activity Bar]																																						
290 Program Management Services																																												
+ Pre-Design/Programming Phase																																												
		1,200	01APR02A	04JAN10	10,328,284	[Critical Activity Bar]																																						
291 Project Management Services																																												
+ Pre-Design/Programming Phase																																												
		1,200	01APR02A	04JAN10	15,492,426	[Critical Activity Bar]																																						
292 Reimbursables																																												
+ Pre-Design/Programming Phase																																												
		1,200	01APR02A	04JAN10	1,156,301	[Critical Activity Bar]																																						
293 Legal Services																																												
+ Pre-Design/Programming Phase																																												
		1,200	01APR02A	04JAN10	1,603,859	[Critical Activity Bar]																																						

Start Date 01JAN02  
 Finish Date 14MAR11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:32

[Green Bar] Early Bar  
 [Blue Bar] Progress Bar  
 [Red Bar] Critical Activity

7E01  
 LACCD  
 East Los Angeles College  
 Campus Summary

Sheet 20 of 21

Date	Revision	Checked	Approved

