




Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010											
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A									
Los Angeles Harbor College																																																					
Total		2,669	03JAN01A	01JUN11	225,123,192	[Gantt bars for 2007-2010]																																															
370 Master Planning																																																					
+ Master Plan																																																					
		801	23AUG01A	22SEP04A	906,644	[Gantt bars for 2007-2010]																																															
381 Environmental Impact Report (EIR)																																																					
+ EIR / CEQA																																																					
		1,240	01APR02A		367,337	[Gantt bars for 2007-2010]																																															
380 Site Survey & Infrastructure Studies																																																					
+ Site Survey & Infrastructure Studies																																																					
		1,037	01OCT01A	05OCT05A	200,000	[Gantt bars for 2007-2010]																																															
300 Program Development & Execution Strategy																																																					
+ Program / Project Management																																																					
		2,279	03JAN02A	01DEC10	0	[Gantt bars for 2007-2010]																																															
301 Liberal Arts Building																																																					
+ Pre-Design / Programming																																																					
		25	26SEP02A	30OCT02A	40,804	[Gantt bars for 2007-2010]																																															
302 Business Building																																																					
+ Pre-Design / Programming																																																					
		102	09DEC02A	29APR03A	40,430	[Gantt bars for 2007-2010]																																															
303 Physics Building																																																					
+ Pre-Design / Programming																																																					
		102	09DEC02A	29APR03A	42,250	[Gantt bars for 2007-2010]																																															
304 Sciences Building																																																					
+ Pre-Design / Programming																																																					
		218	09DEC02A	08OCT03A	42,201	[Gantt bars for 2007-2010]																																															
+ Program / Project Management																																																					
		2,265*	09DEC02A	19FEB09	0	[Gantt bars for 2007-2010]																																															
+ Project Design																																																					
		191	09OCT03A	06JUL04A	622,005	[Gantt bars for 2007-2010]																																															

Start Date 25JAN01  
 Finish Date 01JUN11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:20

 Early Bar  
 Progress Bar  
 Critical Activity

0701  
 LACCD  
 Los Angeles Harbor College  
 Campus Summary

Sheet 1 of 21

Date	Revision	Checked	Approved







Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

309 Student Cafeteria and Seahawk Center

+ Pre-Design / Programming					
		84	02JAN03A	29APR03A	60,030
+ Project Design					
		169	24OCT03A	18JUN04A	22,617




311 Surface Parking Lot & New Loop Road

+ Pre-Design / Programming					
		227	15OCT02A	27AUG03A	11,921
+ Program / Project Management					
		1,512*	15OCT02A	04DEC06A	0
+ Project Design					
		176	18SEP03A	21MAY04A	229,495
+ Project DSA Review					
		149	24MAY04A	23DEC04A	42,176
+ Project Bid and Award					
		119	27DEC04A	13JUN05A	0
+ Project Construction					
		614	08MAR05A	11NOV06A	3,301,623
+ Project Close-Out					
		65	31AUG06A	04DEC06A	26,360
+					
		0	13NOV06A		0

312 Physical Education Facility

+ Pre-Design / Programming					
		314	14JUN02A	27AUG03A	7,230
+ Program / Project Management					
		1,189*	14JUN02A	14SEP05A	0
+ Project Design					
		202	18SEP03A	29JUN04A	15,313
+ Project DSA Review					
		88	29JUN04A	01NOV04A	0
+ Project Bid and Award					
		136	01NOV04A	13MAY05A	0
+ Project Construction					
		79	16MAY05A	06SEP05A	190,461

Start Date 25JAN01  
 Finish Date 01JUN11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:20

 Early Bar  
 Progress Bar  
 Critical Activity

0701

LACCD  
 Los Angeles Harbor College  
 Campus Summary

Sheet 5 of 21

Date	Revision	Checked	Approved











Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

**Nursing Haz Mat Removal**

+ Project Bid and Award					
		0		20DEC04A	0
+ Project Construction					
		25	21DEC04A	26JAN05A	0


**Nursing Interior Package**

+ Project Bid and Award					
		0		18JUL05A	0
+ Project Construction					
		335	19JUL05A	09NOV06A	0
+ Project Close-Out					
		27	13NOV06A	20DEC06A	4,733
+ FF&E					
		147	20MAR06A	13OCT06A	48,031

+					
		0	20MAR06A		0

**329 Administration Building**

+ Pre-Design / Programming					
		975	09DEC02A	27SEP06A	55,700
+ Program / Project Management					
		2,510*	09DEC02A	22OCT09	0
+ Project Design					
		197	28SEP06A	09JUL07	397,032
+ Project DSA Review					
		257	10JUL07	11JUL08	33,136
+ Project Bid and Award					
		113	14JUL08	19DEC08	0
+ Project Construction					
		364	27MAR08	28AUG09	3,855,508
+ Project Close-Out					
		47	31AUG09	04NOV09	28,311
+ FF&E					
		157	17DEC08	29JUL09	893,000
+					
		0	17DEC08		0

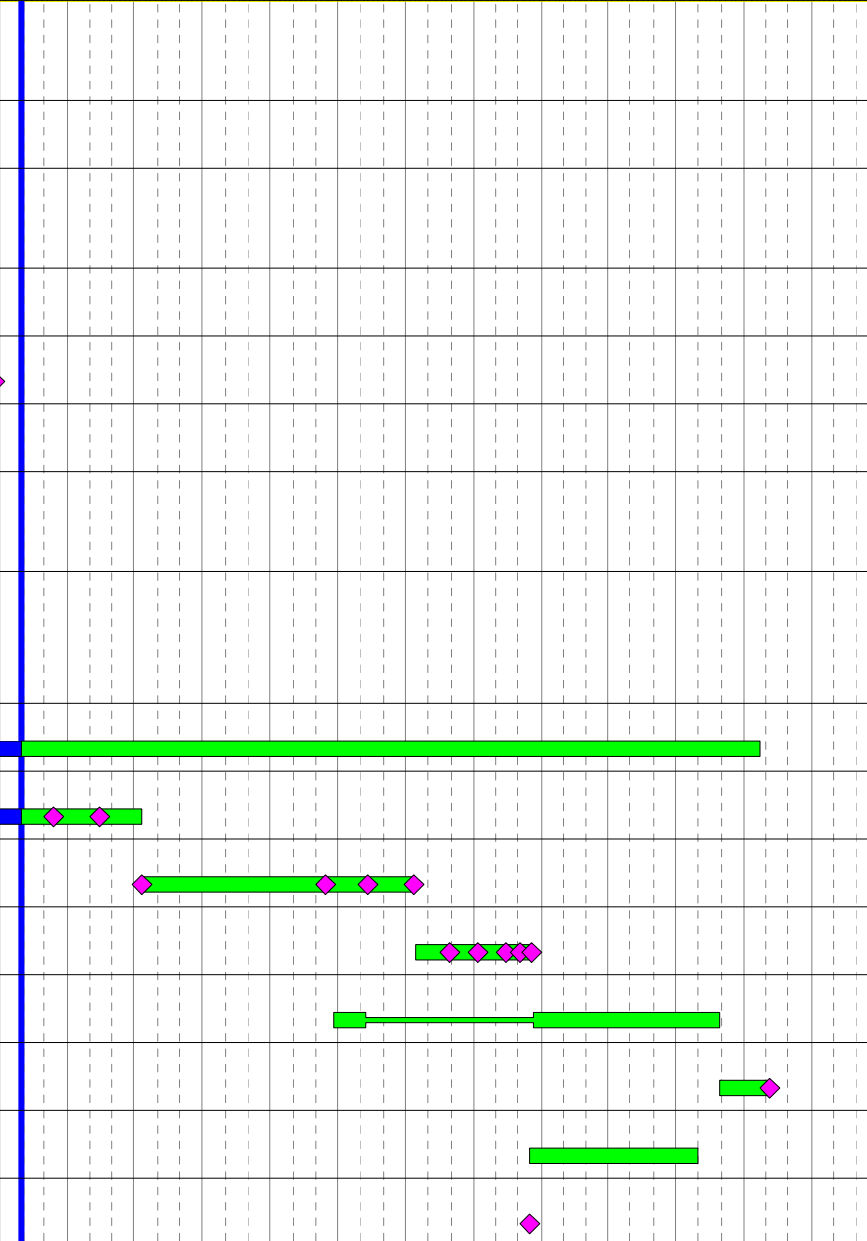

Start Date 25JAN01  
 Finish Date 01JUN11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:20

Early Bar  
 Progress Bar  
 Critical Activity

0701  
 LACCD  
 Los Angeles Harbor College  
 Campus Summary

Sheet 11 of 21

Date	Revision	Checked	Approved





Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Program / Project Management																																												
		1,367*	01JUL03A	28MAR07	0																																							
+ Project Design																																												
		465	01JUL03A	21APR05A	817,999																																							
+ Project Bid and Award																																												
		207	22NOV04A	14SEP05A	71,752																																							
+ Project Construction																																												
		528	14SEP05A	23FEB07	8,308,670																																							
+ Project Close-Out																																												
		124	02OCT06A	28MAR07	62,399																																							
+																																												
		0	02OCT06A		0																																							
338 Site Development																																												
+ Pre-Design / Programming																																												
		854	03DEC02A	02APR06A	0																																							
+ Program / Project Management																																												
		2,543*	03DEC02A	18NOV09	0																																							
+ Project Design																																												
		330	01OCT03A	14JAN05A	94,005																																							
+ Project Bid and Award																																												
		407	10MAR05A	13OCT06A	0																																							
+ Project Construction																																												
		726	29JUL08	01JUN11	883,710																																							
+ Project Close-Out																																												
		145	24APR09	18NOV09	5,431																																							
+																																												
		0	24APR09		0																																							
339 Central Plant																																												
Central Plant - General																																												
+ Pre-Design / Programming																																												
		115	02JAN04A	11JUN04A	0																																							
+ Program / Project Management																																												
		1,476*	02JAN04A	16JAN08	0																																							
+ Project Design																																												
		201	14JUN04A	29MAR05A	513,343																																							
+ Project DSA Review																																												
		302	08MAR05A	12MAY06A	51,980																																							

Start Date 25JAN01  
 Finish Date 01JUN11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:20

Early Bar  
 Progress Bar  
 Critical Activity

0701  
 LACCD  
 Los Angeles Harbor College  
 Campus Summary

Sheet 14 of 21

Date	Revision	Checked	Approved







Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Program / Project Management						[Green bar from Jan 2007 to Dec 2010]																																						
		1,655*	01MAY06A	10NOV10	0																																							
+ Project Design						[Green bar from May 2007 to Mar 2008]																																						
		217	23MAY07	31MAR08	1,432,017																																							
+ Project DSA Review						[Green bar from Apr 2008 to Mar 2009]																																						
		251	01APR08	25MAR09	125,880																																							
+ Project Bid and Award						[Green bar from Mar 2009 to Aug 2009]																																						
		103	26MAR09	19AUG09	0																																							
+ Project Construction						[Green bar from Aug 2009 to Sep 2010]																																						
		277	21AUG09	23SEP10	13,844,026																																							
+ Project Close-Out						[Green bar from Sep 2010 to Nov 2010]																																						
		34	24SEP10	10NOV10	94,348																																							
+ Commissioning						[Green bar from Jul 2010 to Sep 2010]																																						
		57*	29JUL10	23SEP10	137,324																																							
+ FF&E						[Green bar from Aug 2009 to Jul 2010]																																						
		236	24AUG09	28JUL10	1,424,265																																							
+						[Green bar from Aug 2009 to Aug 2009]																																						
		0	24AUG09		0																																							
352 Keyless Entry System																																												
+ Pre-Design / Programming						[Green bar from Dec 2003 to May 2005]																																						
		350	31DEC03A	13MAY05A	0																																							
+ Project Design						[Green bar from May 2005 to Oct 2006]																																						
		429	20MAY05A		38,923																																							
+ Project Bid and Award						[Green bar from Jul 2006 to Oct 2006]																																						
		63	31JUL06A	26OCT06A	0																																							
+ Project Construction						[Green bar from Oct 2006 to Mar 2007]																																						
		105	27OCT06A	28MAR07	852,118																																							
+ Project Close-Out						[Green bar from Mar 2007 to Apr 2007]																																						
		10	29MAR07	11APR07	7,124																																							
353 Off-Site Improvements																																												
+ Project Design						[Green bar from May 2002 to Nov 2008]																																						
		1,650	29MAY02A	06NOV08	510,452																																							
372 Emerg Lghtng, Fire Alarm & Security System																																												
+ Project Construction						[Green bar from Jul 2002 to Oct 2002]																																						
		78	08JUL02A	23OCT02A	5,290																																							

Start Date 25JAN01  
 Finish Date 01JUN11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:20

[Green bar] Early Bar  
 [Blue bar] Progress Bar  
 [Red bar] Critical Activity




0701  
 LACCD  
 Los Angeles Harbor College  
 Campus Summary

Sheet 18 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
373 Central Campus Landscape																																												
+ Pre-Design / Programming																																												
		192	03DEC02A	27AUG03A	33,355																																							
+ Program / Project Management																																												
		2,921*	03DEC02A	01DEC10	0																																							
+ Project Design																																												
		970	04SEP03A	25JUN07	385,258																																							
+ Project DSA Review																																												
		156	26JUN07	06FEB08	26,965																																							
+ Project Bid and Award																																												
		85	07FEB08	05JUN08	0																																							
+ Project Construction																																												
		616	06JUN08	05NOV10	2,881,316																																							
+ Project Close-Out																																												
		17	08NOV10	01DEC10	21,146																																							
378 Land Acquisition																																												
+ Land Acquisition																																												
		1,188	12JUN02A		50,000																																							
379 Campus Improvements (Telephone/Ext. Paint)																																												
Telephone System																																												
+ Project Design																																												
		20	01MAY02A	28MAY02A	0																																							
+ Project Construction																																												
		138	29MAY02A	08DEC02A	1,201,838																																							
Exterior Painting																																												
+ Pre-Design / Programming																																												
		86	15NOV02A	14MAR03A	12,951																																							
+ Project Design																																												
		111	11DEC02A	14MAY03A	136,152																																							
+ Project Bid and Award																																												
		49	05MAY03A	10JUL03A	0																																							
+ Project Construction																																												
		75	11JUL03A	23OCT03A	610,620																																							
+ Project Close-Out																																												
		15	24OCT03A	13NOV03A	0																																							

Start Date 25JAN01  
 Finish Date 01JUN11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:20

 Early Bar  
 Progress Bar  
 Critical Activity

0701

LACCD  
 Los Angeles Harbor College  
 Campus Summary

Sheet 19 of 21

Date	Revision	Checked	Approved



