

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
Los Angeles Southwest College																																												
Total		2,304	14MAY01A	17MAY10	193,460,373	[Gantt bars with red diamonds]																																						
Student Services, Education Center																																												
Student Services Education Center																																												
+ Pre-Design / Programming																																												
		102	15AUG01A	09JAN02A	0																																							
+ Project Design																																												
		330	10JAN02A	23APR03A	1,108,167																																							
+ Project DSA Review																																												
		245	09MAY02A	23APR03A	80,040																																							
+ Project Bid and Award																																												
		83	07MAY03A	03SEP03A	0																																							
+ Project Construction																																												
		548	22SEP03A	10NOV05A	13,595,736																																							
+ FF&E																																												
		386	15DEC04A	15JUN06A	1,033,224																																							
+ Project Close-Out																																												
		350	25OCT05A	09MAR07	0	[Green bar]																																						
Student Services Building Roof Screenwall																																												
+ Project Bid and Award																																												
		59	19APR06A	12JUL06A	0																																							
+ Project Construction																																												
		124	26JUN06A	20DEC06A	148,766																																							
+ Project Close-Out																																												
		33	21DEC06A	07FEB07	0	[Blue diamond]																																						
Cox Building																																												
Cox Building - 4th Floor																																												
+ Pre-Design / Programming																																												
		12	03SEP02A	18SEP02A	7,500																																							
+ Project Design																																												
		31	19SEP02A	31OCT02A	0																																							
+ Project DSA Review																																												
		16	01NOV02A	22NOV02A	0																																							
+ Project Bid and Award																																												
		39	25NOV02A	22JAN03A	0																																							
+ Project Construction																																												
		43	20FEB03A	21APR03A	43,174																																							

Start Date 25JAN01
 Finish Date 17MAY10
 Data Date 31JAN07
 Run Date 02MAR07 12:27

[Green bar] Early Bar
 [Blue bar] Progress Bar
 [Red bar] Critical Activity

S017
 LACCD
 Los Angeles Southwest College
 Campus Summary

Sheet 1 of 14

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

Physical Education Gymnasium

PE Gym, Pool, Bleachers

+ Pre-Design / Programming

	480	12AUG02A	30JUN04A	86,356
--	-----	----------	----------	--------

+ Project Design

	772	01DEC03A	06DEC06A	374,342
--	-----	----------	----------	---------

+ Project DSA Review

	633	02NOV04A	25APR07	17,698
--	-----	----------	---------	--------

+ Project Bid and Award

	78	26APR07	15AUG07	0
--	----	---------	---------	---

+ Project Construction

	156	16AUG07	27MAR08	1,623,144
--	-----	---------	---------	-----------

+ FF&E

	30	15FEB08	27MAR08	138,968
--	----	---------	---------	---------

+ Project Close-Out

	101	28MAR08	19AUG08	0
--	-----	---------	---------	---

PE Gym Acoustic/Sound System

+ Pre-Design / Programming

	350	12AUG02A	29DEC03A	0
--	-----	----------	----------	---

+ Project Design

	320	10DEC03A	09MAR05A	139,441
--	-----	----------	----------	---------

+ Project DSA Review

	267	02NOV04A	16NOV05A	2,265
--	-----	----------	----------	-------

+ Project Bid and Award

	57	18NOV05A	08FEB06A	0
--	----	----------	----------	---

+ Project Construction

	91	09FEB06A	16JUN06A	394,200
--	----	----------	----------	---------

+ Project Close-Out

	205	05JUN06A	26MAR07	0
--	-----	----------	---------	---

PE Gym Re-Roofing (SMP Project)

+ Project DSA Review

	0		04OCT06A	0
--	---	--	----------	---

+ Project Bid and Award


	51	31JAN07	11APR07	0
--	----	---------	---------	---

+ Project Construction

	86	12APR07	13AUG07	473,500
--	----	---------	---------	---------

+ Project Close-Out

	51	14AUG07	24OCT07	0
--	----	---------	---------	---

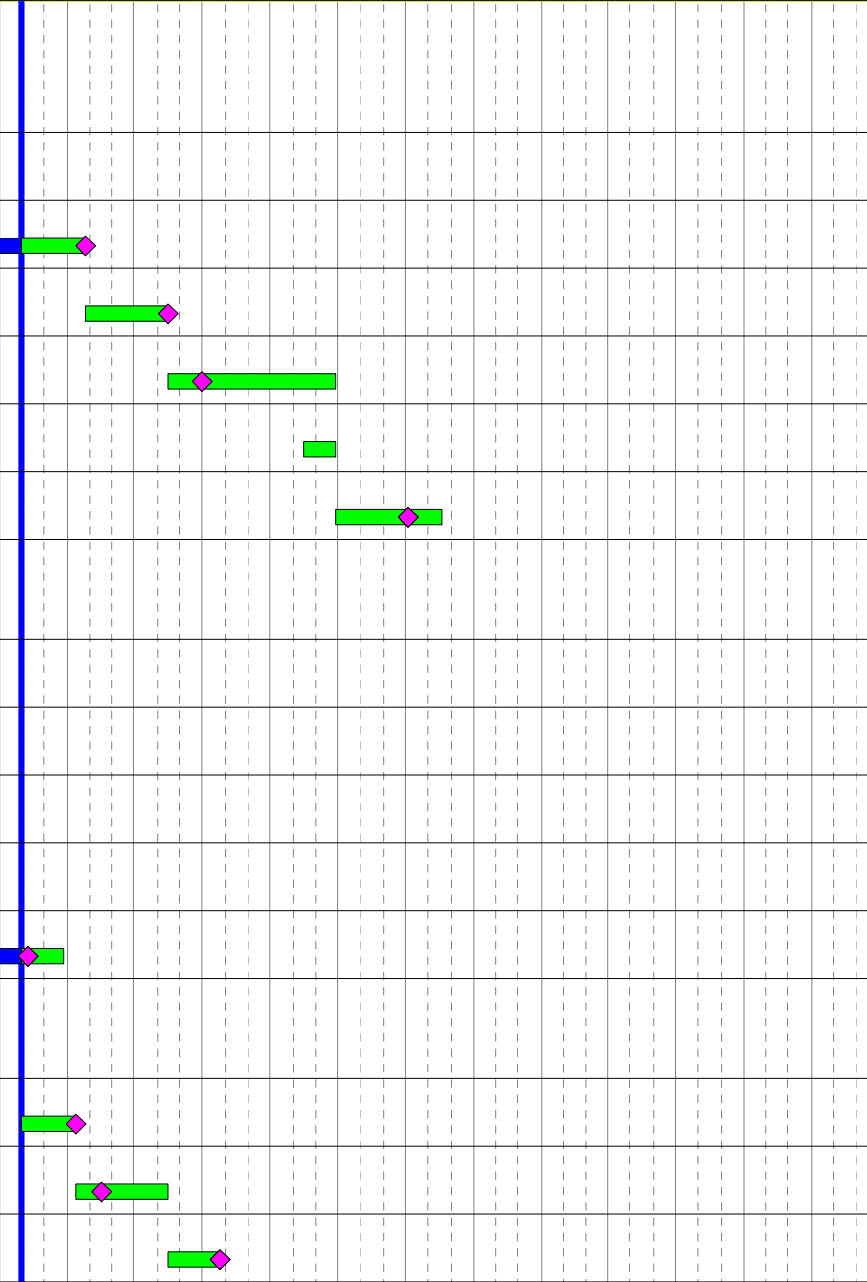

Start Date 25JAN01
 Finish Date 17MAY10
 Data Date 31JAN07
 Run Date 02MAR07 12:27

Early Bar
 Progress Bar
 Critical Activity

S017
 LACCD
 Los Angeles Southwest College
 Campus Summary

Sheet 3 of 14

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

Physical Education Fields and Courts


+ Pre-Design / Programming					
		481	12AUG02A	01JUL04A	18,065
+ Project Design					
		758	01DEC03A	14NOV06A	461,607

Technology Education Center - Modernization

+ Pre-Design / Programming					
		318	12AUG02A	10NOV03A	102,000
+ Project Design					
		748	01DEC03A	31OCT06A	1,271,955
+ Project DSA Review					
		286	27FEB06A	11APR07	60,154
+ Project Bid and Award					
		54	12APR07	27JUN07	0
+ Project Construction					
		268	28JUN07	17JUL08	7,494,360
+ FF&E					
		198	30OCT07	08AUG08	752,563
+ Project Close-Out					
		96	18JUL08	03DEC08	0

Child Development Center

+ Pre-Design / Programming					
		16	02JAN03A	23JAN03A	0
+ Project Design					
		269	03JAN03A	23JAN04A	1,564,519
+ Project DSA Review					
		297	01DEC03A	26JAN05A	141,078
+ Project Bid and Award					
		137	04JAN05A	15JUL05A	0
+ Project Construction					
		466	16JUN05A	13APR07	17,753,600
+ FF&E					
		282	06APR06A	15MAY07	1,200,000
+ Project Close-Out					
		130	09MAR07	11SEP07	0

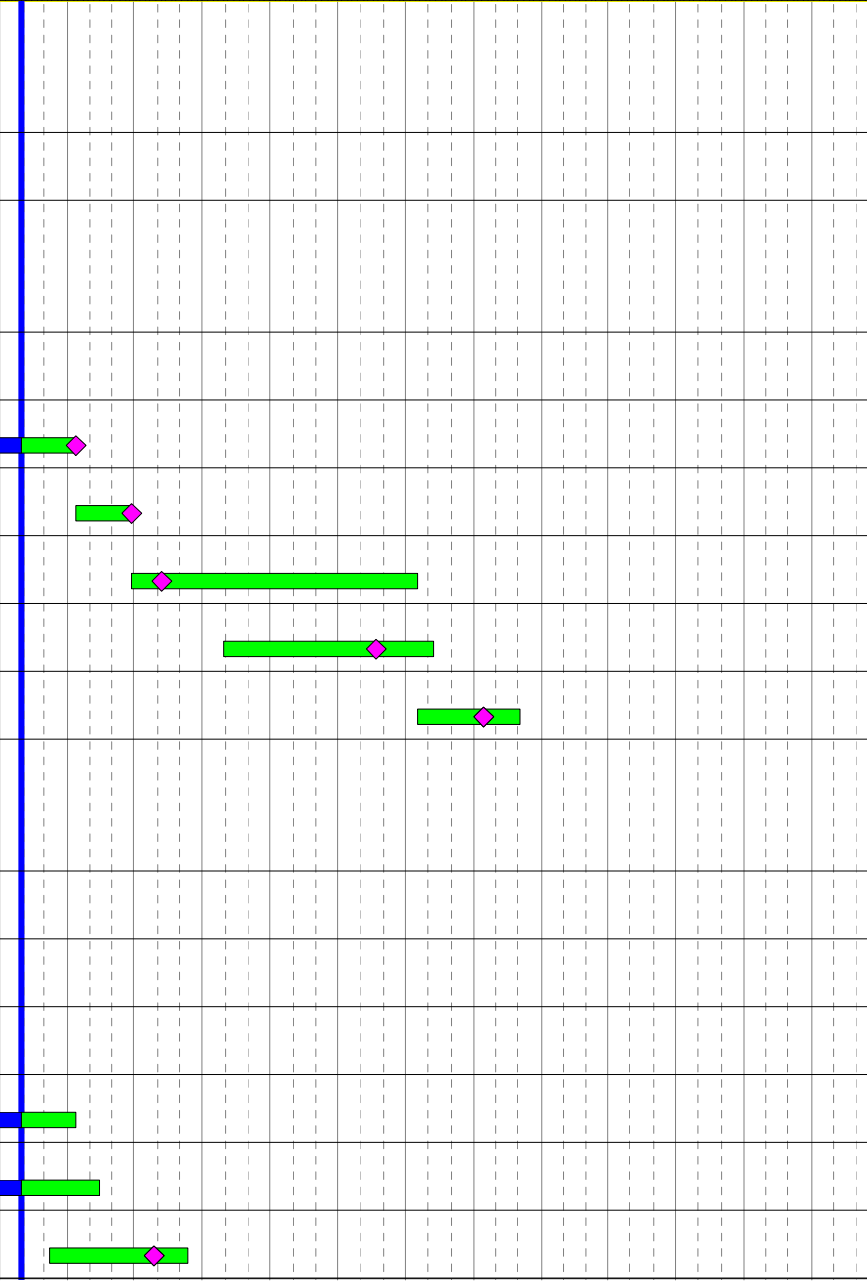

Start Date 25JAN01
 Finish Date 17MAY10
 Data Date 31JAN07
 Run Date 02MAR07 12:27

Early Bar
 Progress Bar
 Critical Activity

S017
 LACCD
 Los Angeles Southwest College
 Campus Summary

Sheet 4 of 14

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Commissioning																																												
Lecture Laboratory Building																																												
Lecture Laboratory Building Modernization																																												
+ Pre-Design / Programming																																												
		318	12AUG02A	10NOV03A	103,000																																							
+ Project Design																																												
		748	01DEC03A	31OCT06A	1,666,491																																							
+ Project DSA Review																																												
		286	27FEB06A	11APR07	78,108																																							
+ Project Bid and Award																																												
		54	12APR07	27JUN07	0																																							
+ Project Construction																																												
		366	28JUN07	05DEC08	8,580,798																																							
+ FF&E																																												
		195	03MAR08	05DEC08	584,372																																							
+ Project Close-Out																																												
		79	08DEC08	30MAR09	0																																							
Lecture Laboratory Building Door Replmnt																																												
+ Project Design																																												
		1	03SEP02A	03SEP02A	0																																							
+ Project DSA Review																																												
		1	10SEP02A	10SEP02A	0																																							
+ Project Bid and Award																																												
		27	24SEP02A	30OCT02A	0																																							
+ Project Construction																																												
		133	31OCT02A	09MAY03A	49,764																																							
+ Project Close-Out																																												
		17	12MAY03A	04JUN03A	0																																							
Central Plant																																												
+ Project Design																																												
		166	06DEC06A	31JUL07	714,504																																							
+ Project DSA Review																																												
		80	23MAY07	14SEP07	0																																							
+ Project Construction																																												
		295	01AUG07	26SEP08	8,633,594																																							
+ Project Close-Out																																												
		55	29SEP08	16DEC08	0																																							

Start Date 25JAN01
 Finish Date 17MAY10
 Data Date 31JAN07
 Run Date 02MAR07 12:27

Early Bar
 Progress Bar
 Critical Activity

S017

LACCD
 Los Angeles Southwest College
 Campus Summary

Sheet 5 of 14

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Commissioning																																												
Campus Improvements East & West Sides																																												
Design-Build - Maintenance & Operations Facility																																												
+ Pre-Design / Programming																																												
+ Project Design																																												
+ Project DSA Review																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ FF&E																																												
+ Project Close-Out																																												
+ Commissioning																																												
Design-Build - Parking Structure																																												
+ Pre-Design / Programming																																												
+ Project Design																																												
+ Project DSA Review																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ FF&E																																												
+ Project Close-Out																																												
Design-Build - Campus Security Facility																																												
+ Pre-Design / Programming																																												

Start Date 25JAN01
 Finish Date 17MAY10
 Data Date 31JAN07
 Run Date 02MAR07 12:27

Early Bar
 Progress Bar
 Critical Activity

S017
 LACCD
 Los Angeles Southwest College
 Campus Summary




Sheet 6 of 14

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

Demolition					
Demolition - Northeast Quadrant					
+ Pre-Design / Programming					
		113*	11JUN03A	01OCT03A	0
+ Project Design					
		293*	22OCT03A	09AUG04A	197,206
+ Project DSA Review					
		206	01DEC03A	17SEP04A	5,630
+ Project Bid and Award					
		59	22SEP04A	15DEC04A	0
+ Project Construction					
		122	13DEC04A	01JUN05A	1,236,839
+ Project Close-Out					
		136	26FEB05A	08SEP05A	0
Demolition of Bungalows for Interim Parking					
+ Project Design					
		8	23MAY05A	02JUN05A	35,114
+ Project Bid and Award					
		27	06JUN05A	13JUL05A	0
+ Project Construction					
		58	08JUN05A	29AUG05A	205,640
+ Project Close-Out					
		145	29AUG05A	22MAR06A	0
Demolition of Bungalows for Interim Prkg Ph 1.1					
+ Project Design					
		46	21NOV05A	25JAN06A	29,449
+ Project Bid and Award					
		39	30DEC05A	22FEB06A	0
+ Project Construction					
		46	17FEB06A	21APR06A	264,174
+ Project Close-Out					
		60	24APR06A	18JUL06A	0
Demolition of Bungalows for Interim Prkg Ph 1.2					
+ Project Design					
		54	28JUN06A	13SEP06A	25,640
+ Project Bid and Award					
		27	12SEP06A	18OCT06A	0
+ Project Construction					
		39	02OCT06A	27NOV06A	116,390

Start Date 25JAN01
 Finish Date 17MAY10
 Data Date 31JAN07
 Run Date 02MAR07 12:27

 Early Bar
 Progress Bar
 Critical Activity

S017
 LACCD
 Los Angeles Southwest College
 Campus Summary

Date	Revision	Checked	Approved

