

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
Los Angeles Valley College																																												
Total		2,852	19FEB02A	10APR13	285,614,345	[Red hatched bar]																																						
805 Maintenance & Operations, Sheriffs Station																																												
+ Project Design																																												
		288	25NOV02A	20JAN04A	807,173																																							
+ Project DSA Review																																												
		204	01MAR04A	16DEC04A	56,508																																							
+ Project Bid and Award																																												
		94	09DEC04A	25APR05A	0																																							
+ Project Construction																																												
		233	26APR05A	27MAR06A	7,732,556																																							
+ Commissioning																																												
		910	17OCT03A	17MAY07	80,000	[Green bar]																																						
+ FF&E																																												
		305*	12JAN05A	27MAR06A	1,008,560																																							
+ Project Close-Out																																												
		248	28MAR06A	13MAR07	0	[Green bar] [Purple diamond]																																						
817 Foreign Language Building																																												
+ Project Design																																												
		309	30JAN03A	20APR04A	159,177																																							
+ Project DSA Review																																												
		179	09JUN04A	24FEB05A	10,742																																							
+ Project Bid and Award																																												
		74	25FEB05A	09JUN05A	0																																							
+ Project Construction																																												
		189	30NOV04A	29AUG05A	1,141,837																																							
+ FF&E																																												
		112*	23MAR05A	29AUG05A	203,818																																							
+ Project Close-Out																																												
		245	24AUG05A	09AUG06A	0																																							
875 Restrooms																																												
Priority Restrooms																																												
+ Pre-Design / Programming																																												
		66*	30JAN03A	02MAY03A	0																																							
+ Project Design																																												
		391	29APR02A	12NOV03A	223,736																																							

Start Date 18FEB02
 Finish Date 10APR13
 Data Date 31JAN07
 Run Date 02MAR07 12:18

[Green bar] Early Bar
 [Blue bar] Progress Bar
 [Red bar] Critical Activity

0107
 LACCD
 Los Angeles Valley College
 Campus Summary

Sheet 1 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Design																																												
		366	18JAN05A	23JUN06A	391,909																																							
+ Project DSA Review																																												
		152	23JUN06A	25JAN07A	18,128																																							
+ Project Bid and Award																																												
		938	31JAN07	17SEP10	0																																							
+ Project Construction																																												
		174	20JUL07	21MAR08	1,924,860																																							
+ FF&E																																												
		235*	25APR07	21MAR08	1,391,554																																							
+ Project Close-Out																																												
		40	24MAR08	16MAY08	0																																							
Camp Imp - Exterior Painting Projects																																												
+ Project Design																																												
		149	24MAR04A	21OCT04A	85,848																																							
+ Project Bid and Award																																												
		266	18OCT04A	05NOV05A	8,292																																							
+ Project Construction																																												
		399	24FEB05A	15SEP06A	844,230																																							
+ Project Close-Out																																												
		335	09JUN05A	29SEP06A	0																																							
823 Motion Picture - TV Studio Expansion																																												
+ Project Design																																												
		338	09MAY05A	04SEP06A	174,147																																							
+ Project DSA Review																																												
		162	28JUN06A	13FEB07	8,690																																							
+ Project Bid and Award																																												
		93	29JAN07A	06JUN07	0																																							
+ Project Construction																																												
		200	07JUN07	17MAR08	1,174,720																																							
+ Project Close-Out																																												
		80	18MAR08	08JUL08	0																																							
825 Gymnasium Complex																																												
+ Pre-Design / Programming																																												
		277	25FEB02A	31MAR03A	107,514																																							
+ Project Design																																												
		631	30JAN03A	29JUL05A	2,411,291																																							

Start Date 18FEB02
 Finish Date 10APR13
 Data Date 31JAN07
 Run Date 02MAR07 12:18

Early Bar
 Progress Bar
 Critical Activity

0107




LACCD
 Los Angeles Valley College
 Campus Summary

Sheet 6 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project DSA Review																																												
		353	29JUL05A	13DEC06A	126,664																																							
+ Project Bid and Award																																												
		209	09MAY06A	28FEB07	0																																							
+ Project Construction																																												
		265	01FEB07	11FEB08	13,703,164																																							
+ Commissioning																																												
		240	22MAY08	27APR09	0																																							
+ FF&E																																												
		318*	24MAY06A	16AUG07	1,520,830																																							
+ Project Close-Out																																												
		200	17AUG07	26MAY08	0																																							
803 Allied Health and Science Center																																												
+ Pre-Design / Programming																																												
		296	25FEB02A	25APR03A	241,560																																							
+ Project Design																																												
		579	02DEC02A	21MAR05A	7,217,993																																							
+ Project DSA Review																																												
		327	06AUG04A	21NOV05A	200,659																																							
+ Project Bid and Award																																												
		199	01JUL05A	13APR06A	0																																							
+ Project Construction																																												
		604	09DEC05A	14APR08	35,213,580																																							
+ Commissioning																																												
		1,469	27OCT03A	27JUL09	238,000																																							
+ FF&E																																												
		606*	07DEC05A	14APR08	5,042,930																																							
+ Project Close-Out																																												
		80	15APR08	05AUG08	0																																							
802 Library and Learning Resource Center																																												
+ Pre-Design / Programming																																												
		537	25FEB02A	09APR04A	299,404																																							
+ Project Design																																												
		1,168	30JAN03A	03SEP07	3,770,204																																							
+ Project DSA Review																																												
		173	01OCT07	30MAY08	238,000																																							

Start Date 18FEB02
 Finish Date 10APR13
 Data Date 31JAN07
 Run Date 02MAR07 12:18

 Early Bar
 Progress Bar
 Critical Activity

0107

LACCD
 Los Angeles Valley College
 Campus Summary

Sheet 7 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Bid and Award																																												
		167	02JUN08	23JAN09	0																																							
+ Project Construction																																												
		970	31JAN07	02NOV10	32,484,750																																							
+ Commissioning																																												
		2,032	12APR04A	12MAR12	208,000																																							
+ FF&E																																												
		554*	16JUL08	07SEP10	4,596,856																																							
+ Project Close-Out																																												
		40	08SEP10	02NOV10	0																																							
801 Media Arts Center																																												
+ Pre-Design / Programming																																												
		593	25FEB02A	29JUN04A	188,625																																							
+ Project Design																																												
		1,270	31JAN03A	28JAN08	2,252,761																																							
+ Project DSA Review																																												
		158	29JAN08	05SEP08	79,455																																							
+ Project Bid and Award																																												
		93	08SEP08	16JAN09	0																																							
+ Project Construction																																												
		565	02APR08	09JUN10	10,847,729																																							
+ Commissioning																																												
		1,934	20FEB04A	05SEP11	183,000																																							
+ FF&E																																												
		421*	22OCT08	09JUN10	3,072,100																																							
+ Project Close-Out																																												
		80	10JUN10	30SEP10	0																																							
820 Art Building																																												
Art Building Gallery Ceiling																																												
+ Project Design																																												
		164	09JUL03A	03MAR04A	0																																							
+ Project DSA Review																																												
		96	04MAR04A	19JUL04A	989																																							
+ Project Bid and Award																																												
		81	06AUG04A	01DEC04A	1,800																																							
+ Project Construction																																												
		58	02DEC04A	25FEB05A	217,608																																							

Start Date 18FEB02
 Finish Date 10APR13
 Data Date 31JAN07
 Run Date 02MAR07 12:18

Early Bar
 Progress Bar
 Critical Activity

0107

LACCD
 Los Angeles Valley College
 Campus Summary

Sheet 8 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Construction																																												
821 Music Building																																												
+ Pre-Design / Programming																																												
+ Project Design																																												
+ Project DSA Review																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ FF&E																																												
+ Project Close-Out																																												
816 Humanities Building																																												
+ Pre-Design / Programming																																												
+ Project Design																																												
+ Project DSA Review																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ FF&E																																												
+ Project Close-Out																																												
812 Business Journalism																																												
+ Pre-Design / Programming																																												

Start Date 18FEB02
 Finish Date 10APR13
 Data Date 31JAN07
 Run Date 02MAR07 12:18

Early Bar
 Progress Bar
 Critical Activity

0107

LACCD
 Los Angeles Valley College
 Campus Summary

Sheet 11 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
Temp Fac - Temp Trailer for Overflow																																												
+ Project DSA Review																																												
		5	31JAN07	06FEB07	0																																							
+ Project Bid and Award																																												
		40	07FEB07	03APR07	27,180																																							
+ Project Construction																																												
		60	04APR07	26JUN07	137,545																																							
+ Project Close-Out																																												
		20	27JUN07	25JUL07	0																																							
Temp Fac - Food Service																																												
+ Project Design																																												
		2,252	06JUL04A	10APR13	63,195																																							
+ Project Construction																																												
		1,481	16JUL07	10APR13	0																																							
Temp Fac - Move Bus Office from Campus Cntr																																												
+ Project Design																																												
		199	25AUG05A	06JUN06A	0																																							
+ Project Bid and Award																																												
		246	17MAR06A	28FEB07	0																																							
+ Project Construction																																												
		149	25JAN07A	22AUG07	52,378																																							
+ Project Close-Out																																												
		30	23AUG07	03OCT07	0																																							
Temp Fac - Field House/Lockers																																												
+ Project Design																																												
		100	03DEC09	23APR10	0																																							
+ Project Construction																																												
		100	26APR10	13SEP10	60,222																																							
+ Project Close-Out																																												
		90	14SEP10	19JAN11	0																																							
Temp Fac - Cost to Date																																												
+ Pre-Design / Programming																																												
		44	08MAR02A	08MAY02A	0																																							
+ Project Design																																												
		107	08MAR02A	07AUG02A	0																																							
+ Project DSA Review																																												
		44	22MAR02A	22MAY02A	0																																							
+ Project Bid and Award																																												
		311	08MAR02A	30MAY03A	0																																							

Start Date 18FEB02
Finish Date 10APR13
Data Date 31JAN07
Run Date 02MAR07 12:18

Early Bar
 Progress Bar
 Critical Activity

0107
LACCD
Los Angeles Valley College
Campus Summary

Sheet 15 of 21

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
RWGPL - Discretionary & Miscellaneous Fund																																												
+ Project Construction																																												
		855	31MAR04A	07AUG07	100,000																																							
RWGPL - Phase 1 Landscaping (Tree Trimming)																																												
+ Project Design																																												
		271	03OCT03A	28OCT04A	13,233																																							
+ Project Bid and Award																																												
		110	31MAY04A	02NOV04A	0																																							
+ Project Construction																																												
		31	04NOV04A	20DEC04A	117,214																																							
+ Project Close-Out																																												
		122	21DEC04A	15JUN05A	0																																							
RWGPL - Phase 1 Courtyard, Monuments and Graphic																																												
+ Project Design																																												
		422	01MAR04A	27OCT05A	654,198																																							
+ Project DSA Review																																												
		158	31JAN07	10SEP07	0																																							
+ Project Bid and Award																																												
		92	04SEP07	11JAN08	0																																							
+ Project Construction																																												
		383	11OCT06A	04APR08	0																																							
+ Project Close-Out																																												
		20	07APR08	02MAY08	0																																							
RWGPL - Phase 1 Marquee																																												
+ Project Design																																												
		30	02MAY05A	13JUN05A	0																																							
+ Project DSA Review																																												
		95	14JUN05A	26OCT05A	0																																							
+ Project Bid and Award																																												
		84	24OCT05A	22FEB06A	0																																							
+ Project Construction																																												
		149	13FEB06A	08SEP06A	0																																							
+ Project Close-Out																																												
		20	11SEP06A	07NOV06A	0																																							
RWGPL - Phase 1 Center and Art Courtyard																																												
+ Project Design																																												
		52	02FEB05A	15APR05A	0																																							
+ Project DSA Review																																												
		159	06MAY05A	21DEC05A	16,995																																							

Start Date 18FEB02
 Finish Date 10APR13
 Data Date 31JAN07
 Run Date 02MAR07 12:18

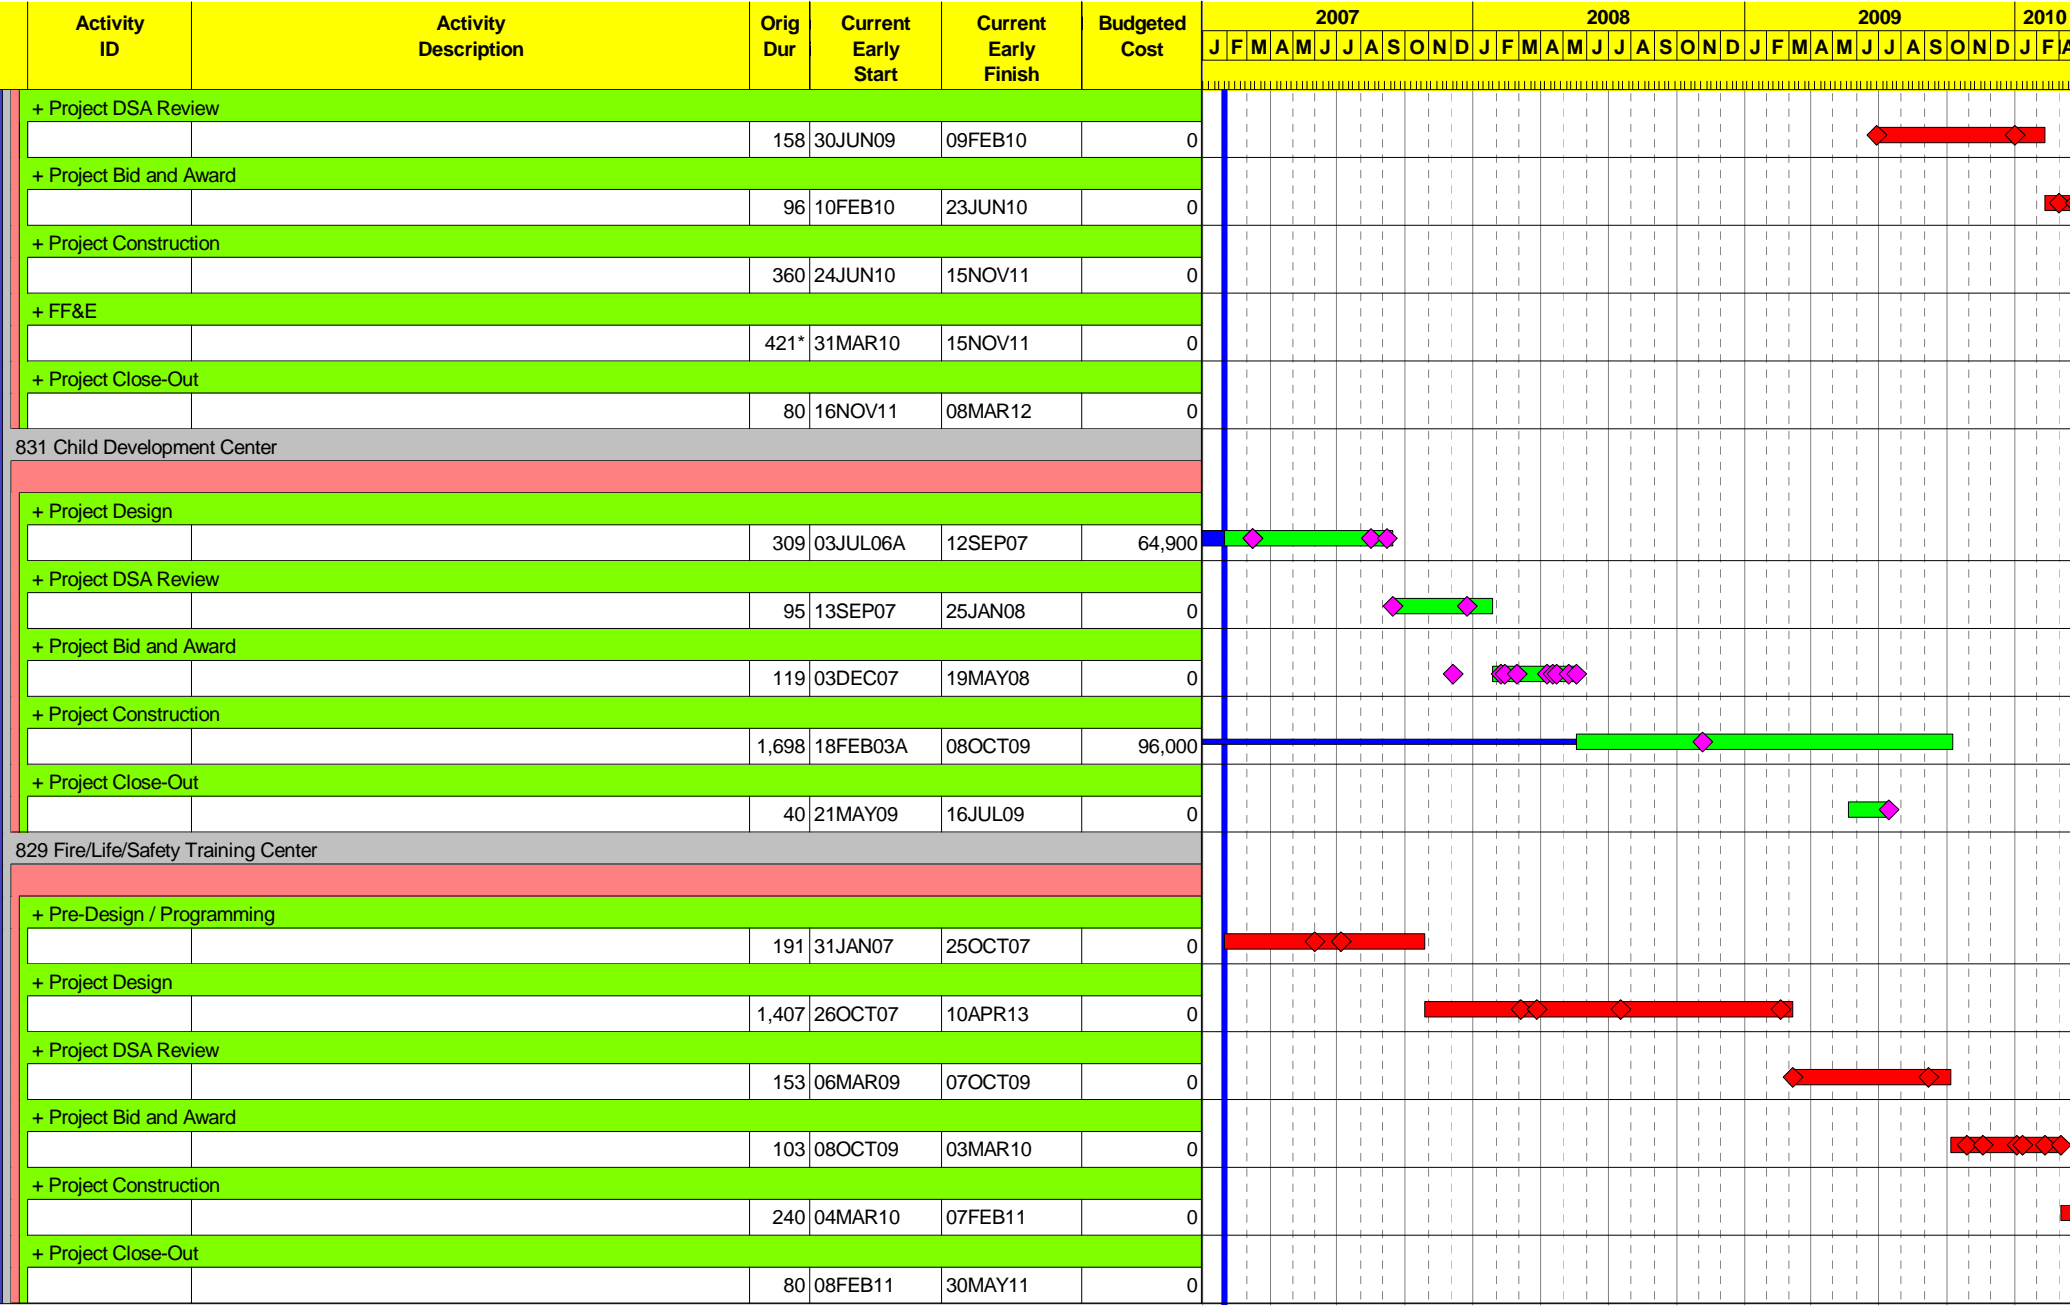
Early Bar
 Progress Bar
 Critical Activity

0107




LACCD
 Los Angeles Valley College
 Campus Summary

Sheet 17 of 21

Date	Revision	Checked	Approved



Start Date 18FEB02
 Finish Date 10APR13
 Data Date 31JAN07
 Run Date 02MAR07 12:18

 Early Bar
 Progress Bar
 Critical Activity

0107

LACCD
 Los Angeles Valley College
 Campus Summary

Sheet 19 of 21

Date	Revision	Checked	Approved

