

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010											
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A									
Los Angeles Pierce College																																																					
Total																																																					
501 Center for the Sciences																																																					
Center for the Sciences																																																					
+ Pre-Design/Programming																																																					
+ Project Design																																																					
+ Project DSA Review																																																					
+ Project Bid and Award																																																					
+ Project Construction																																																					
+ FF&E																																																					
+ Project Close-Out																																																					
+ Commissioning																																																					
502 Life Science/Chemistry/Physics Bldg (NOM)																																																					
+ Pre-Design/Programming																																																					
+ Project Design																																																					
+ Project DSA Review																																																					
+ Project Bid and Award																																																					
+ Project Construction																																																					
+ FF&E																																																					
+ Project Close-Out																																																					

Start Date 01JAN00
 Finish Date 21JUL11
 Data Date 29JAN07
 Run Date 02MAR07 12:22

Early Bar
 Progress Bar
 Critical Activity

P107
 LACCD
 Los Angeles Pierce College
 Campus Summary

Sheet 1 of 19

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

+ Project Construction					
		288*	21APR10	02FEB11	2,242,535
+ FF&E					
		28*	06JAN11	02FEB11	111,535
+ Project Close-Out					
		169*	03FEB11	21JUL11	0

508 Library- Capital Outlay Project

Library Phase I

+ Project Bid and Award					
		140	05JUL06A		16,200
+ Project Construction					
		15	11DEC06A	05JAN07A	0
+ FF&E					
		92	15SEP06A	01FEB07	0
+ Project Close-Out					
		60	02FEB07	26APR07	0




509 Child Development Center

+ Pre-Design/Programming					
		375	01JAN02A	25JUN03A	0
+ Project Design					
		643	25JUN03A	05JAN06A	437,534
+ Project DSA Review					
		1	06JAN06A	06JAN06A	41,486
+ Project Bid and Award					
		1	09JAN06A	09JAN06A	3,500
+ Project Construction					
		1	10JAN06A	10JAN06A	4,518,977
+ FF&E					
		1	10JAN06A	10JAN06A	278,900

509 Child Development Center

+ Pre-Design/Programming					
		521	01JAN02A	26JAN04A	58,580
+ Project Design					
		388	27JAN04A	29JUL05A	0
+ Project DSA Review					
		753	25MAY06A	15MAY09	241,521
+ Project Close-Out					
		527	18MAY05A	13JUN07	0

Start Date 01JAN00
 Finish Date 21JUL11
 Data Date 29JAN07
 Run Date 02MAR07 12:22

 Early Bar
 Progress Bar
 Critical Activity

P107
 LACCD
 Los Angeles Pierce College
 Campus Summary

Date	Revision	Checked	Approved


Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

510 Beh. Sci./Soc. Sci./Math/English Bldgs (NOM)

+ Pre-Design/Programming					
		351	01JAN02A	22MAY03A	31,474
+ Project Design					
		1,129	23MAY03A	26OCT07	351,358
+ Project DSA Review					
		234*	29OCT07	18JUN08	30,130
+ Project Bid and Award					
		147*	25NOV09	20APR10	1,800
+ Project Construction					
		288*	21APR10	02FEB11	3,275,598
+ FF&E					
		20*	06JAN11	02FEB11	208,994
+ Project Close-Out					
		169*	03FEB11	21JUL11	0

513 Business Education (SOM)

Business Education					
+ Pre-Design/Programming					
		355	01JAN02A	28MAY03A	3,075
+ Project Design					
		1,005	29MAY03A	11MAY07	220,919
+ Project DSA Review					
		183	14MAY07	05FEB08	137,903
+ Project Bid and Award					
		110	23JAN08	24JUN08	16,200
+ Project Construction					
		200	25JUN08	09APR09	1,777,039
+ FF&E					
		20	13MAR09	09APR09	80,820
+ Project Close-Out					
		125	10APR09	01OCT09	0
Business Education - Cinemalab					
+ Pre-Design/Programming					
		187	01JAN02A	23SEP02A	0
+ Project Design					
		45	02SEP02A	01NOV02A	21,990
+ Project DSA Review					
		89	02NOV02A	19MAR03A	1,585

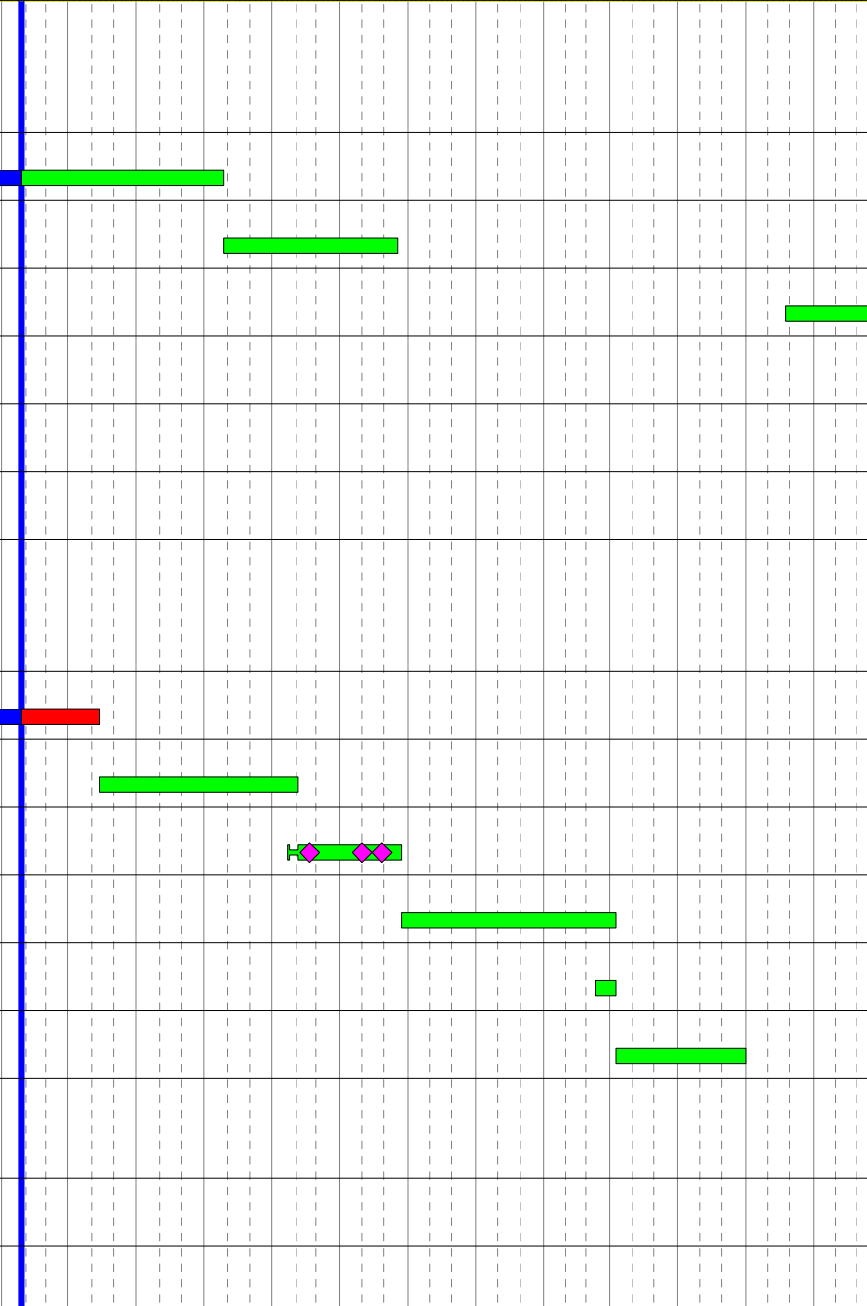

Start Date 01JAN00
 Finish Date 21JUL11
 Data Date 29JAN07
 Run Date 02MAR07 12:22

Early Bar
 Progress Bar
 Critical Activity

P107
 LACCD
 Los Angeles Pierce College
 Campus Summary

Sheet 5 of 19

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

519 Maintenance & Operations Facility

Central

+ Pre-Design/Programming		1,285	01JAN02A		52,425
--------------------------	--	-------	----------	--	--------

Gardening

+ Pre-Design/Programming		545	01JAN02A	27FEB04A	1,000
--------------------------	--	-----	----------	----------	-------

+ Project Design		235	01MAR04A	31JAN05A	1,606,016
------------------	--	-----	----------	----------	-----------

+ Project Close-Out		286	05JAN06A	20FEB07	0
---------------------	--	-----	----------	---------	---

Refrigeration

+ Pre-Design/Programming		1,285	01JAN02A		13,006
--------------------------	--	-------	----------	--	--------

Automotive

+ Pre-Design/Programming		1,285	01JAN02A		21,150
--------------------------	--	-------	----------	--	--------

Above Ground Fuel Storage

+ Project Design		134	19APR05A	21OCT05A	0
------------------	--	-----	----------	----------	---

+ Project Bid and Award		89	21OCT05A	02MAR06A	0
-------------------------	--	----	----------	----------	---

+ Project Construction		110	28FEB06A	31JUL06A	0
------------------------	--	-----	----------	----------	---

+ Project Close-Out		95	31JUL06A	13DEC06A	0
---------------------	--	----	----------	----------	---

521 Horticulture Building


+ Pre-Design/Programming		2,426	01JAN02A	21JUL11	44,475
--------------------------	--	-------	----------	---------	--------

+ Project Design		235	01MAR04A	31JAN05A	1,943,286
------------------	--	-----	----------	----------	-----------

522 Animal Science-Relocation of Animals

+ Pre-Design/Programming		545	01JAN02A	27FEB04A	21,275
--------------------------	--	-----	----------	----------	--------

+ Project Design		880	01MAR04A	10AUG07	1,285,850
------------------	--	-----	----------	---------	-----------

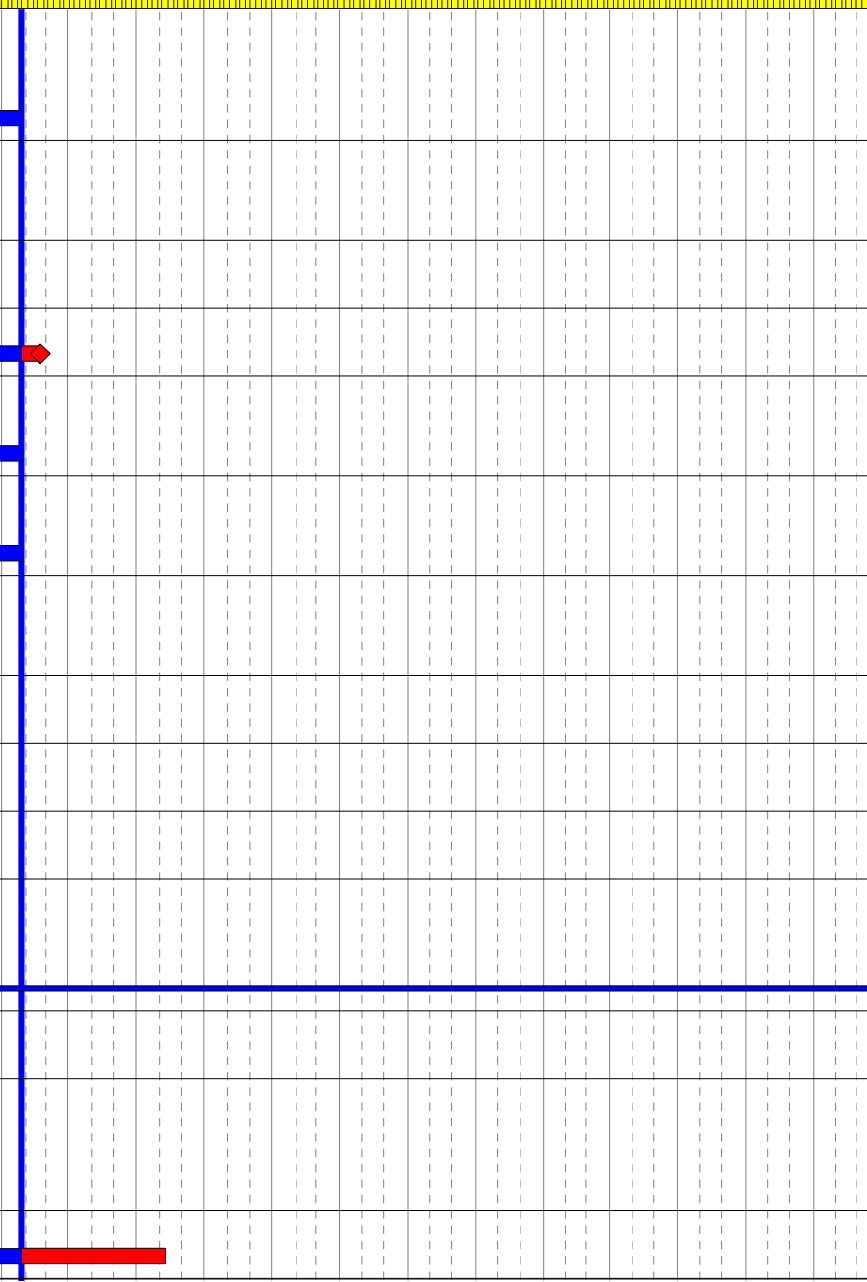

Start Date 01JAN00
 Finish Date 21JUL11
 Data Date 29JAN07
 Run Date 02MAR07 12:22

Early Bar
 Progress Bar
 Critical Activity

P107
 LACCD
 Los Angeles Pierce College
 Campus Summary

Sheet 8 of 19

Date	Revision	Checked	Approved


Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

(C) Demolition of Soils Lab					
+ Pre-Design/Programming					
		60	07JAN05A	31MAR05A	0
+ Project Design					
		25	01APR05A	05MAY05A	18,828
+ Project Bid and Award					
		62	05MAY05A	29JUL05A	10,190
+ Closed/Completed Projects					
		80	16AUG05A	07DEC05A	381,663




577 Relocation/Acquisition of Temp Facilities					
Swing Space					
+ Pre-Design/Programming					
		349	01JAN02A	20MAY03A	21,961
+ Project Design					
		477	21MAY03A	05APR05A	509,472
+ Project DSA Review					
		422	16FEB05A	06OCT06A	44,138
+ Project Bid and Award					
		673	30NOV04A	24JUL07	18,000
+ Project Construction					
		715	27JAN05A	13NOV07	6,300,536
+ Project Close-Out					
		315	29JAN07	24APR08	0

CPM Trailers					
+ Pre-Design/Programming					
		187	01JAN02A	23SEP02A	0
+ Project Design					
		45	02SEP02A	01NOV02A	5,858
+ Project DSA Review					
		89	02NOV02A	19MAR03A	6,151
+ Project Bid and Award					
		220	20MAR03A	30JAN04A	1,800
+ Project Construction					
		309	02FEB04A	15APR05A	743,489
+ Project Close-Out					
		605	14OCT04A	07MAR07	0

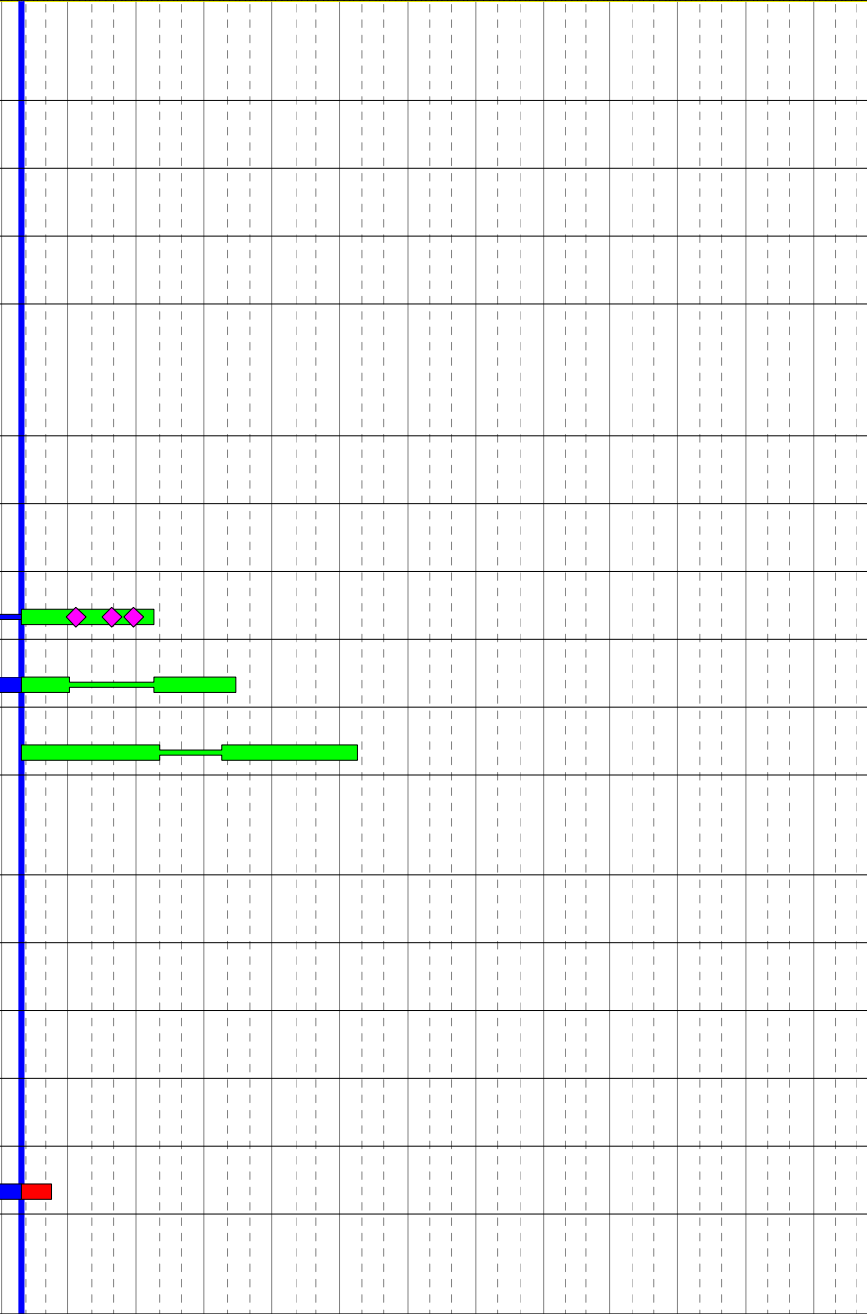Temporary Child Development Center					
+ Project Design					
		64	24JUL03A	21OCT03A	102,795



Start Date 01JAN00
 Finish Date 21JUL11
 Data Date 29JAN07
 Run Date 02MAR07 12:22

 Early Bar
 Progress Bar
 Critical Activity

P107
 LACCD
 Los Angeles Pierce College
 Campus Summary

Sheet 16 of 19

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A

Campus Improvements - Aesthetic Architect

+ Pre-Design/Programming					
		125	28FEB03A	21AUG03A	186,000
+ Project Design					
		1,771	01APR04A	22MAR11	0

Campus Improvements - Central Plant

+ Pre-Design/Programming					
		260	30JUN03A	06JUL04A	36,797
+ Project Design					
		341	07JUL04A	03NOV05A	908,528
+ Project DSA Review					
		330	05DEC05A	27MAR07	137,903
+ Project Bid and Award					
		110	21MAR07	21AUG07	16,200
+ Project Construction					
		245	22AUG07	11AUG08	6,188,596
+ Project Close-Out					
		121	12AUG08	05FEB09	0
+ Commissioning					
		80	22APR08	11AUG08	0

580 Site Survey & Infrastructure Mapping Study

+ Site Survey & Infrastructure Studies					
		559	28SEP01A	17DEC03A	264,892

581 Environmental Impact Report (EIR)


+ EIR/CEQA					
		267	01FEB02A	21FEB03A	647,387

Move Management & Services

+					
		1,635*	29JAN07	21JUL11	1,063,231

Program Management

+					
		3,641*	02AUG01A	21JUL11	10,497,680

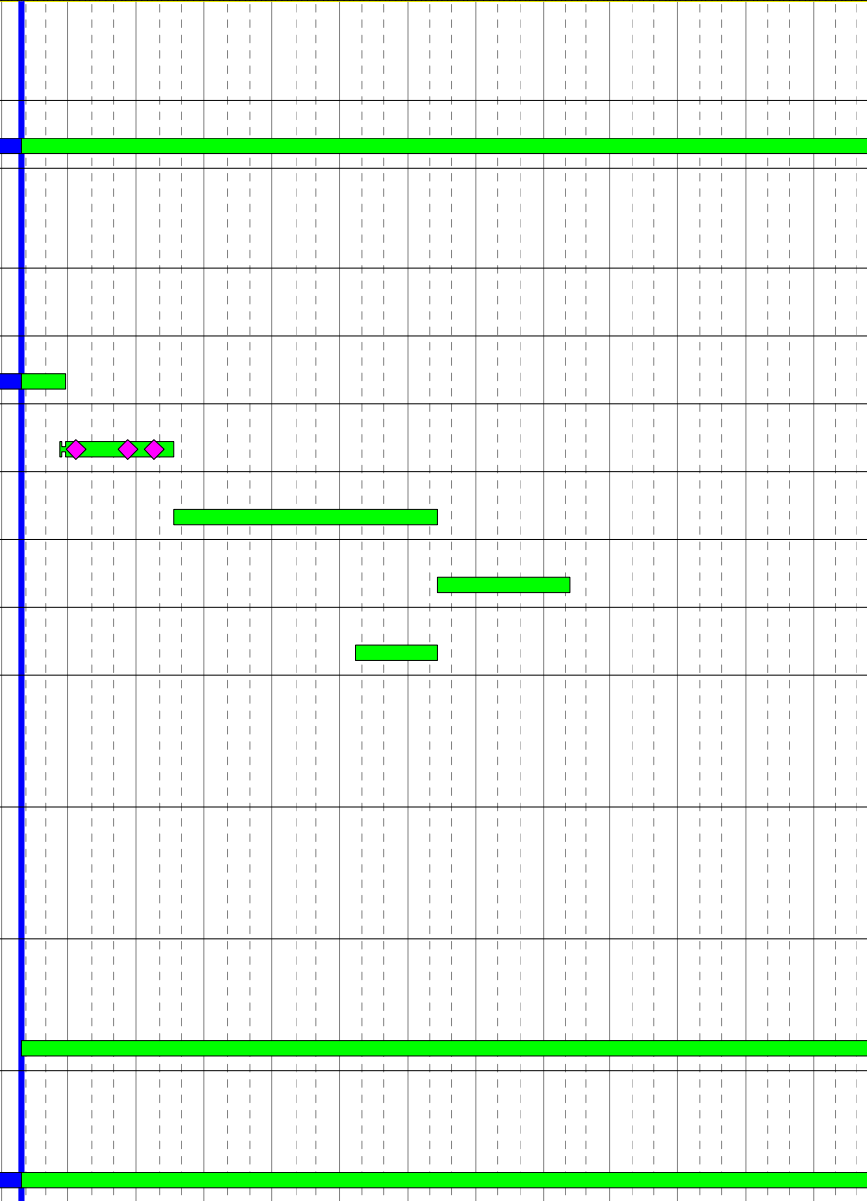

Start Date 01JAN00
 Finish Date 21JUL11
 Data Date 29JAN07
 Run Date 02MAR07 12:22

Early Bar
 Progress Bar
 Critical Activity

P107

LACCD
 Los Angeles Pierce College
 Campus Summary

Sheet 18 of 19

Date	Revision	Checked	Approved

