

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010											
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A									
West Los Angeles College																																																					
Total		2,572	23AUG01A	20OCT11	186,668,928	[Red diamond pattern]																																															
970 Master Planning																																																					
+ Master Plan																																																					
		728	04APR02A	23FEB05A	612,560																																																
981 Environmental Impact Report (EIR)																																																					
EIR/CEQA																																																					
+ EIR / CEQA																																																					
		633	16SEP02A	21MAR05A	3,304,146																																																
Temporary Haul Road/Sound Wall																																																					
+ Project Design																																																					
		475	12APR05A	28FEB07	0	[Blue bar]																																															
+ Project Bid and Award																																																					
		60	01MAR07	23MAY07	0	[Green bar]																																															
+ Project Construction																																																					
		88	23MAY07	26SEP07	3,976,872	[Green bar]																																															
+ Project Close-Out																																																					
		119	25JUN07	12DEC07	0	[Green bar]																																															
Permanent Road/Express Pipe Supply Renovation																																																					
+ Project Design																																																					
		589	13MAY05A	12SEP07	0	[Blue bar]																																															
+ Project Bid and Award																																																					
		74	10DEC07	26MAR08	0	[Green bar]																																															
+ Project Construction																																																					
		185	14APR08	06JAN09	0	[Green bar]																																															
+ Project Close-Out																																																					
		118	07JAN09	24JUN09	0	[Green bar]																																															
980 Site Survey and Infrastructure Studies																																																					
+ Site Survey & Infrastructure Studies																																																					
		295	20DEC02A	24FEB04A	386,985																																																
983 Soil Testing - Methane Gas																																																					
+ Site Survey & Infrastructure Studies																																																					
		34	28JUN04A	13AUG04A	150,000																																																

Start Date 10APR01  
 Finish Date 20OCT11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:28

[Green bar] Early Bar  
 [Blue bar] Progress Bar  
 [Red bar] Critical Activity

WC58  
 LACCD  
 West Los Angeles College  
 Campus Summary


Sheet 1 of 12

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A


905 Parking Structure - Located at Lot 8

+ Pre-Design / Programming					
		226	05DEC01A	25OCT02A	17,000
+ Project Design					
		390	24OCT02A	12MAY04A	2,452,382
+ Project DSA Review					
		554	31OCT03A	11JAN06A	137,807
+ Project Bid and Award					
		60	01MAR07	23MAY07	0
+ Project Construction					
		240	24MAY07	06MAY08	14,039,037
+ Project Close-Out					
		118	07MAY08	22OCT08	6,500

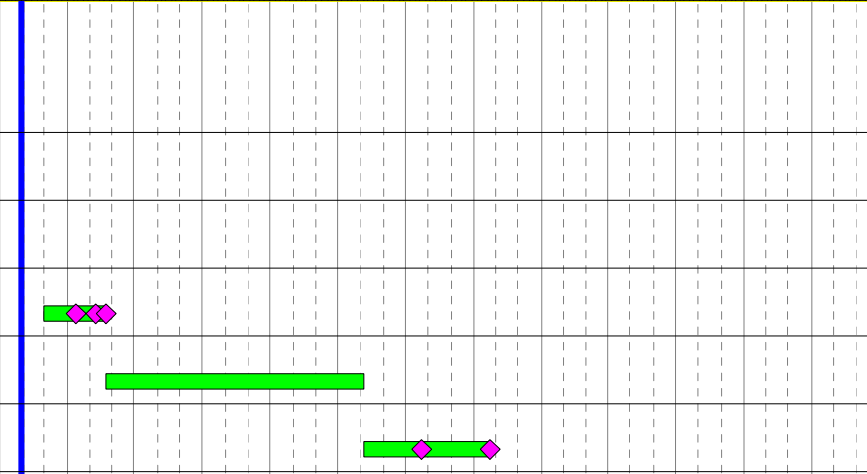


901 Science and Math Building

+ Pre-Design / Programming					
		405	23AUG01A	31MAR03A	75,000
+ Project Design					
		531	02JAN03A	07FEB05A	5,832,291
+ Project DSA Review					
		460	13OCT04A	09AUG06A	328,464
+ Project Bid and Award					
		68	19APR07	25JUL07	0
+ Project Construction					
		440	26JUL07	23APR09	32,843,262
+ FF&E					
		180	06AUG08	23APR09	4,132,940
+ Project Close-Out					
		107	24APR09	23SEP09	0
+ Commissioning					
		1,515	25MAY04A	26MAY10	243,800

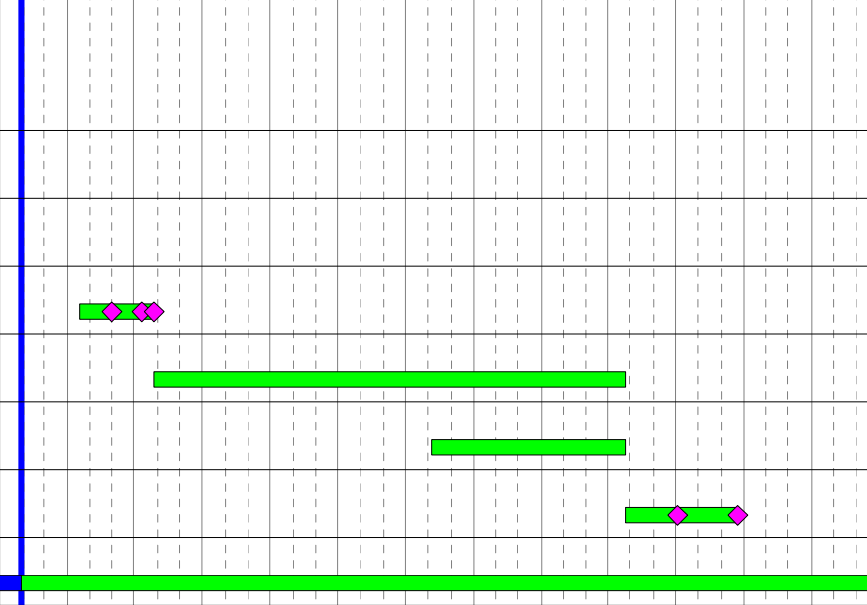




904 Student Services and Administration Bldg

Student Services Building					
+ Pre-Design / Programming					
		161	14AUG02A	04APR03A	240,500
+ Project Design					
		970	05MAR03A	05JAN07A	4,826,551




Start Date 10APR01  
 Finish Date 20OCT11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:28

 Early Bar  
 Progress Bar  
 Critical Activity

WC58  
 LACCD  
 West Los Angeles College  
 Campus Summary

Sheet 2 of 12

Date	Revision	Checked	Approved

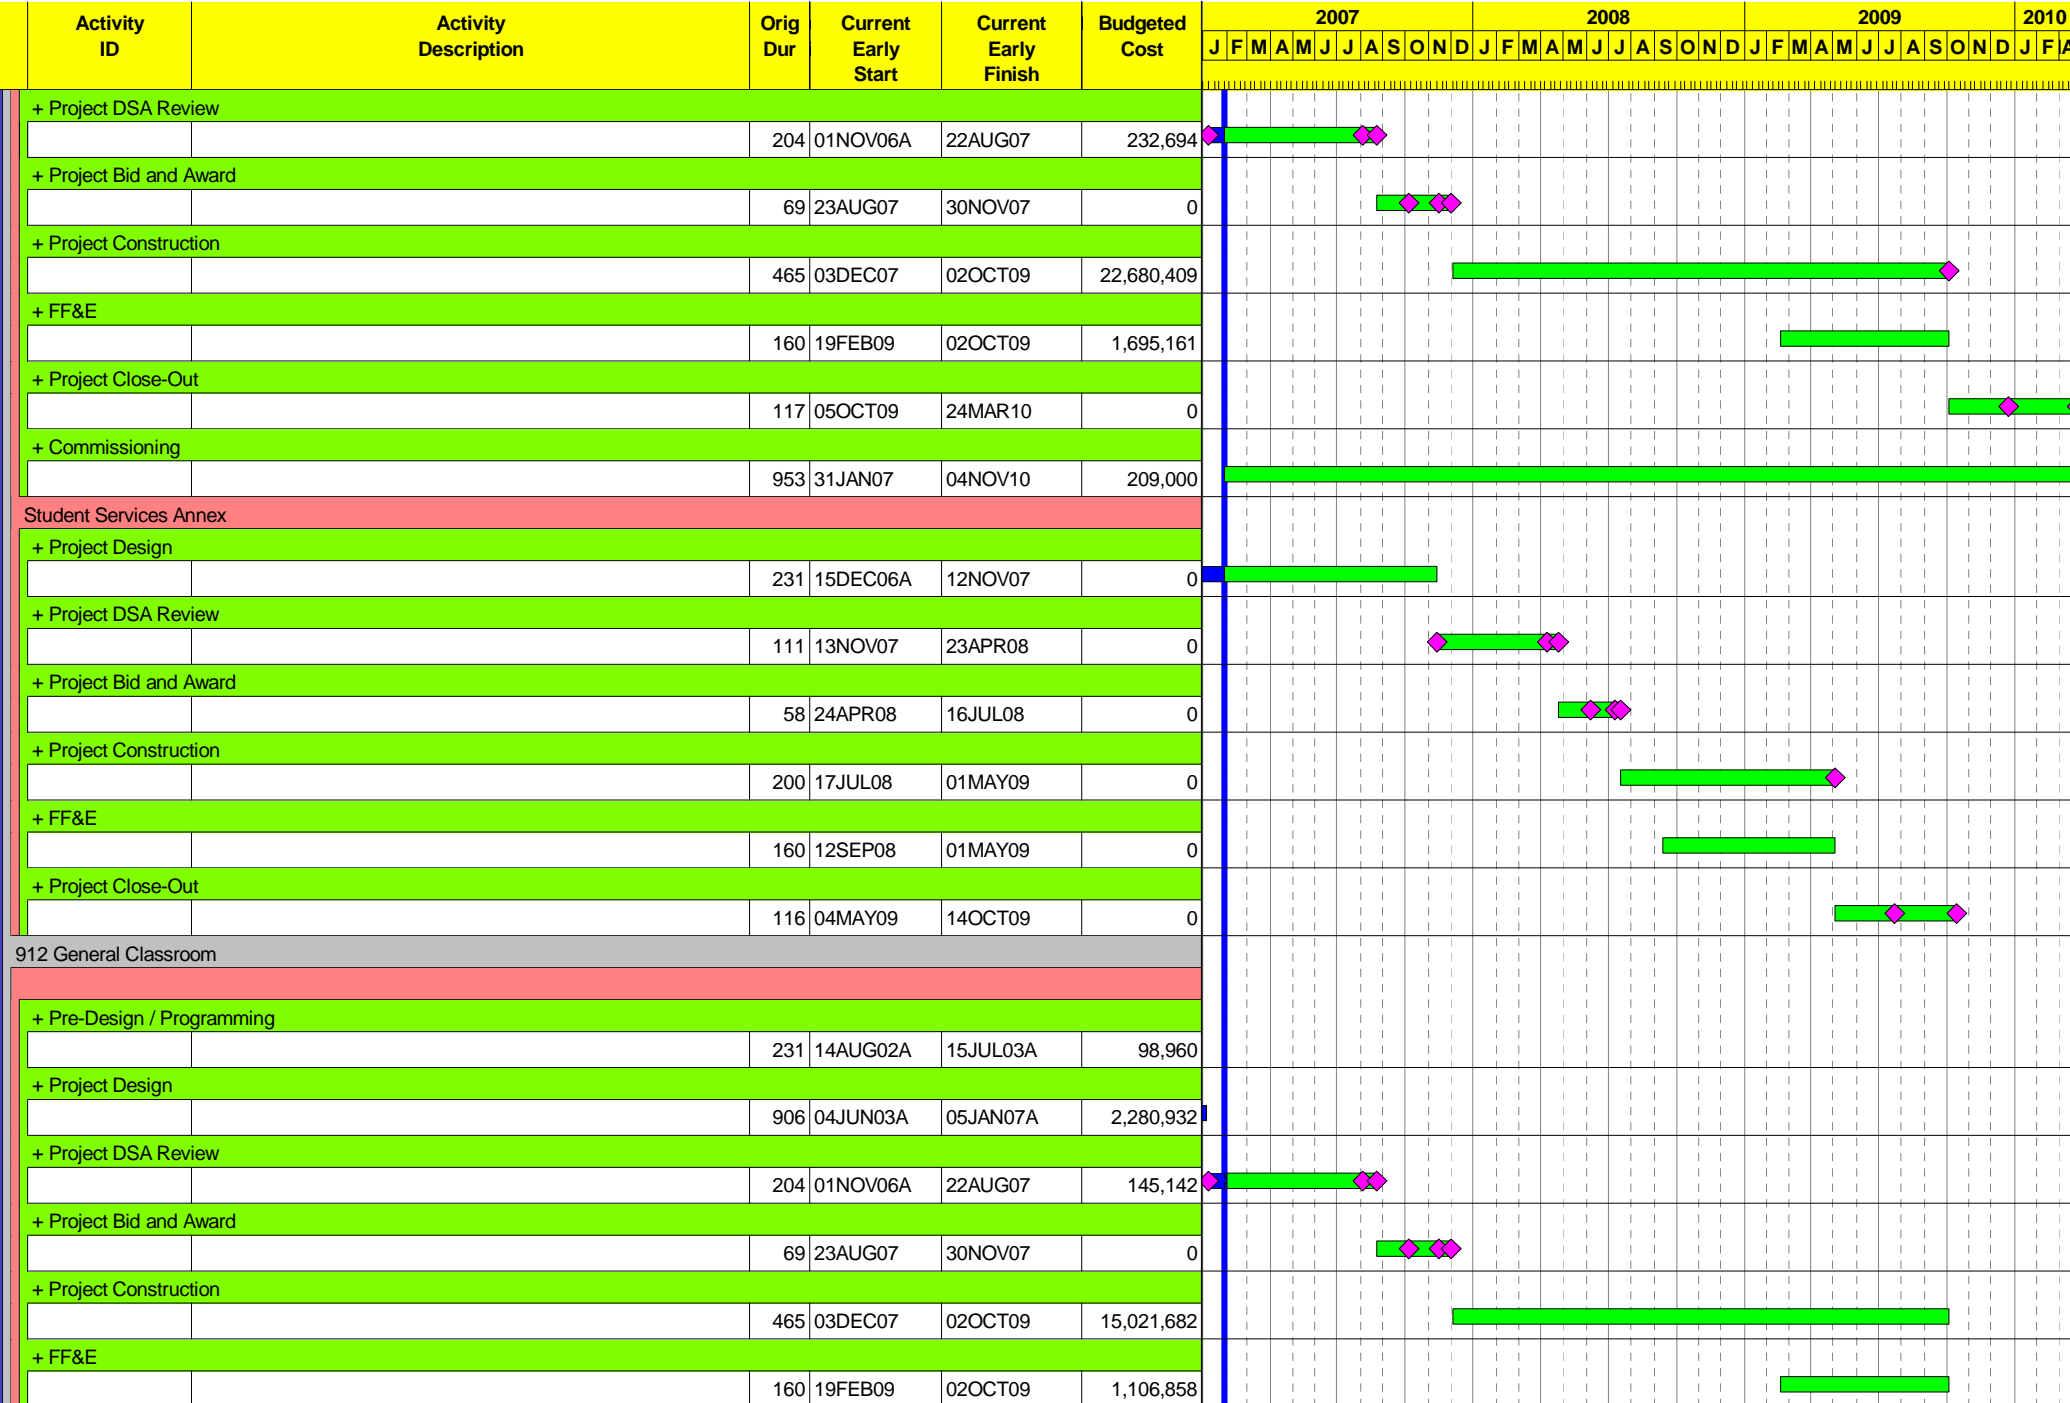

Start Date 10APR01  
 Finish Date 20OCT11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:28

Early Bar  
 Progress Bar  
 Critical Activity

WC58  
 LACCD  
 West Los Angeles College  
 Campus Summary

Date	Revision	Checked	Approved



Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
+ Project Close-Out																																												
909 Entertainment Media Arts																																												
+ Pre-Design / Programming																																												
979 Campus Improvements																																												
Athletic Complex																																												
+ Project Design																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
Utility Infrastructure																																												
+ Project Design																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
Bleachers and Restrooms-Cancelled																																												
+ Project Design																																												
+ Project DSA Review																																												
+ Project Bid and Award																																												
+ Project Construction																																												
+ Project Close-Out																																												
South Entry Plaza																																												
+ Project Design																																												

Start Date 10APR01  
 Finish Date 20OCT11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:28

Early Bar  
 Progress Bar  
 Critical Activity

WC58  
 LACCD  
 West Los Angeles College  
 Campus Summary

Date	Revision	Checked	Approved





Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010		
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A
<b>+ Project Design</b>																																												
		706	28FEB05A	12DEC07	209,348																																							
<b>+ Project Bid and Award</b>																																												
		71	13DEC07	26MAR08	9,864																																							
<b>+ Project Construction</b>																																												
		420	25SEP09	23MAY11	1,047,393																																							
<b>+ Project Close-Out</b>																																												
		87	24MAY11	21SEP11	0																																							
<b>Site Preparation &amp; Albert Vera St Repair</b>																																												
<b>+ Project Design</b>																																												
		378	30SEP02A	31MAR04A	77,436																																							
<b>+ Project Bid and Award</b>																																												
		221	23JAN04A	06DEC04A	4,284																																							
<b>+ Project Construction</b>																																												
		117	06DEC04A	20MAY05A	454,819																																							
<b>+ Project Close-Out</b>																																												
		279	20MAY05A	28JUN06A	0																																							
<b>Men's P.E. Building Renovations-Cancelled</b>																																												
<b>+ Project Design</b>																																												
		371	05JAN04A	21JUN05A	66,871																																							
<b>+ Project DSA Review</b>																																												
		435	22JUN05A	14MAR07	3,603																																							
<b>+ Project Bid and Award</b>																																												
		84	15MAR07	12JUL07	0																																							
<b>+ Project Construction</b>																																												
		50	13JUL07	21SEP07	415,320																																							
<b>+ Project Close-Out</b>																																												
		95	24SEP07	08FEB08	0																																							
<b>Temporary Parking Lot 8A</b>																																												
<b>+ Project Design</b>																																												
		1,123	30SEP02A	14MAR07	23,856																																							
<b>+ Project Bid and Award</b>																																												
		867	02JAN04A	07JUN07	1,261																																							
<b>+ Project Construction</b>																																												
		30	07MAY08	18JUN08	133,898																																							
<b>+ Project Close-Out</b>																																												
		96	19JUN08	03NOV08	0																																							

Start Date 10APR01  
 Finish Date 20OCT11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:28

Early Bar  
 Progress Bar  
 Critical Activity

WC58  
 LACCD  
 West Los Angeles College  
 Campus Summary




Sheet 8 of 12

Date	Revision	Checked	Approved



Activity ID	Activity Description	Orig Dur	Current Early Start	Current Early Finish	Budgeted Cost	2007												2008												2009												2010									
						J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	A							
+ Project Close-Out																								107	24MAY11	19OCT11	0																								
915 Science Building Renovation																																																			
+ Pre-Design / Programming																								806	05JAN04A	14MAR07	12,000																								
+ Project Design																								180	15MAR07	28NOV07	224,188																								
+ Project DSA Review																								198	29NOV07	10SEP08	11,224																								
+ Project Bid and Award																								73	13MAR09	24JUN09	0																								
+ Project Construction																								105	25JUN09	19NOV09	1,191,775																								
+ FF&E																								40	25SEP09	19NOV09	373,808																								
+ Project Close-Out																								137	20NOV09	09JUN10	0																								
972 Call for Assistance Phones																																																			
+ Project Design																								857	30SEP02A	22FEB06A	158,555																								
+ Project Bid and Award																								81	01MAR07	22JUN07	0																								
+ Project Construction																								130	25JUN07	28DEC07	814,570																								
+ Project Close-Out																								88	31DEC07	05MAY08	0																								
973 RWGPL-Roadways, Walkways, Grounds, Parking Lot																																																			
Stocker Street Berm																																																			
+ Project Design																								1,301	30SEP02A	26NOV07	592,904																								
+ Project DSA Review																								181	27NOV07	13AUG08	34,196																								
+ Project Bid and Award																								128	14AUG08	18FEB09	0																								
+ Project Construction																								230	19FEB09	14JAN10	3,320,099																								

Start Date 10APR01  
 Finish Date 20OCT11  
 Data Date 31JAN07  
 Run Date 02MAR07 12:28

 Early Bar  
 Progress Bar  
 Critical Activity

WC58  
 LACCD  
 West Los Angeles College  
 Campus Summary

Sheet 10 of 12

Date	Revision	Checked	Approved



